

Additive Grinding Building

Data as on: 30-Sep-26

AT RISK

Supply vendor: KBL | 2,000 MT + TS 160.9 MT (silos 132.3 + liner 28.6) | Supply Oct-26 -> Feb-27 | Erection Nov-26 -> Jun-27

SCOPE
2,000 MT
+ TS 160.9 MT (silos 132.3 + liner 28.6)

DRAWINGS RELEASED
1,399 MT
70% of scope · 601 MT pending


SUPPLIED TILL SEP
12 MT
Sep actual 12 MT; plan exceeds balance by 12

OCT-DEC SUPPLY PLAN
1,050 MT
53% of scope · 250 / 300 / 500 MT

OCT-DEC ERECTION PLAN
400 MT
20% of scope · 0 erected, starts Nov-26

PEAK MONTHLY RATE (MT)
520 | 300
supply (Jan-27) | erection (May-Jun)

WORK-FRONT SEQUENCE & MONTHLY PLAN (MT)

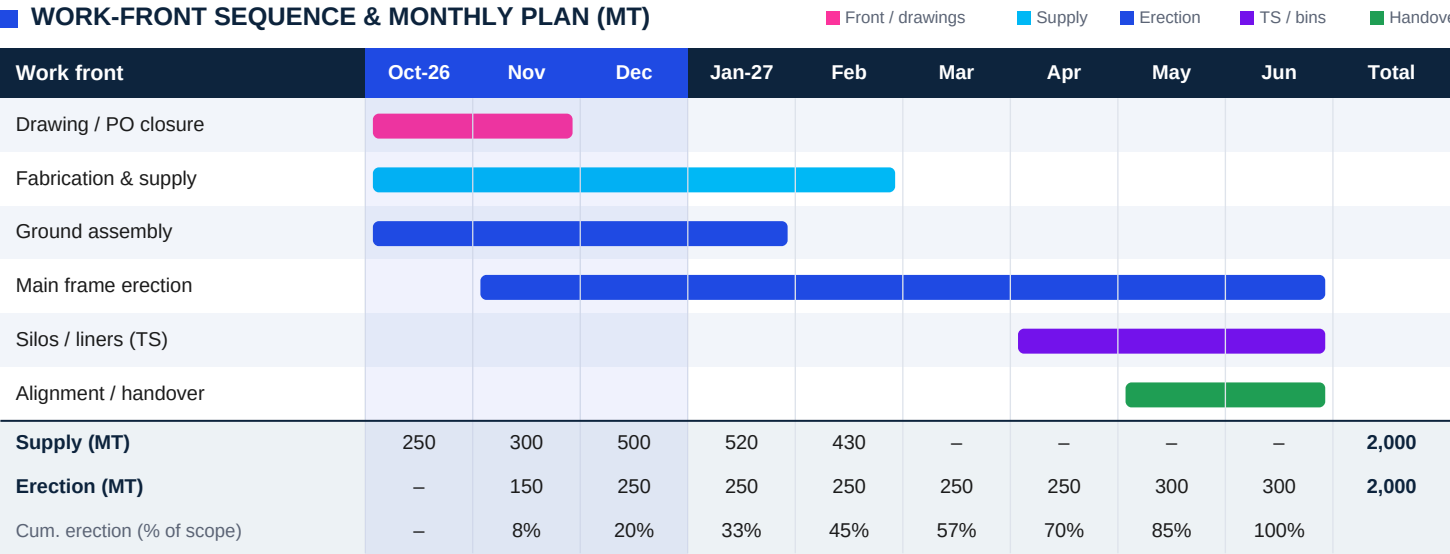

KEY CONCERNS & ACTIONS

DRAWINGS

Only 1,399 of 2,000 MT drawings released; 601 MT (30%) pending. Cumulative supply crosses 1,399 MT in Jan-27.
Action: Close balance drawings / PO by Nov-26 to feed Jan-27 fabrication.

SUPPLY


Oct-26–Feb supply plan totals 2,000 MT but the balance is 1,988 MT (12 MT already done) - quantities not reconciled against scope.
Action: Reconcile the supply plan against scope and the Sep-26 actual.

SUPPLY

Dispatch must jump from 12 MT in Sep-26 to 520 MT/month; Dec and Jan-27 alone need 1,020 MT.
Action: Lock fabrication lot plan; weekly dispatch vs 250/300/500/520/430 MT.


ERECTION

Erection starts Nov-26 and must hold 150–300 MT/month for 8 months.
Action: Mobilise crane and erection crew before Nov-26.



Supply view: Material waiting at site builds to ~1,112 MT by Feb-27 (supply ends 5 months before erection) - plan laydown and erection sequence.

SCOPE vs DRAWINGS vs SUPPLY vs ERECTION (MT)



601 MT drawings pending; 0.6% supplied; erection starts Nov-26.

Screen House / Building

Data as on: 30-Sep-26

AT RISK

Supply vendor: Samal Brothers | 1,019 MT + TS: equipment, crane & conveyor supports | Supply Oct-26 -> Jan-27 | Erection Oct-26 -> Apr-27

SCOPE

1,019 MT

+ TS: equipment, crane & conveyor supports

DRAWINGS RELEASED

1,019 MT

100% of scope · nil pending

SUPPLIED TILL SEP

Nil

Nil in Sep

OCT-DEC SUPPLY PLAN

750 MT

74% of scope · 250 / 250 / 250 MT

OCT-DEC ERECTION PLAN

430 MT

42% of scope · 0 erected, starts Oct-26

PEAK MONTHLY RATE (MT)

269 | 200

supply (Jan-27) | erection (Dec)

WORK-FRONT SEQUENCE & MONTHLY PLAN (MT)

Work front	Oct-26	Nov	Dec	Jan-27	Feb	Mar	Apr	May	Jun	Total
Foundation release	Front / drawings									
Material receipt	Supply	Supply	Supply	Supply						
Starter bay / bracing	Erection	Erection								
Lower tiers		Erection	Erection	Erection						
Screen / crane levels			Erection	Erection	Erection	Erection				
Upper tiers / roof					Erection	Erection	Erection			
Handover							Handover			
Supply (MT)	250	250	250	269	–	–	–	–	–	1,019
Erection (MT)	50	180	200	166	168	160	95	–	–	1,019
Cum. erection (% of scope)	5%	23%	42%	58%	75%	91%	100%	100%	100%	

KEY CONCERNS & ACTIONS

SUPPLY

Dispatch must jump from 0 MT in Sep-26 to 269 MT/month; Oct and Jan-27 alone need 519 MT.
Action: Lock fabrication lot plan; weekly dispatch vs 250/250/250/269 MT.

FRONT

Erection starts first and needs surveyed starter-bay foundations now.
Action: Release surveyed starter-bay foundations / anchor bolts.

ERECTION

Erection starts Oct-26 and must hold 50–200 MT/month for 7 months.
Action: Mobilise crane and erection crew before Oct-26.



Supply view: Material waiting at site builds to ~423 MT by Jan-27 (supply ends 4 months before erection) - plan laydown and erection sequence.

SCOPE vs DRAWINGS vs SUPPLY vs ERECTION (MT)

Scope	1,019 MT
Drawings released	1,019 MT · 100%
Supplied till Sep	Nil
Erected till date	0 MT · starts Oct-26

Drawings complete; supply starts Oct-26; erection starts Oct-26.

Return Fines Building

Data as on: 30-Sep-26

Supply vendor: Vrinda Bhillai (site fabrication) | 393 MT + TS 66.3 MT (bins, liner, weighing bins) | Supply Oct-26 -> Jan-27 | Erection Nov-26 -> Mar-27

AT RISK

SCOPE

393 MT

+ TS 66.3 MT (bins, liner, weighing bins)

DRAWINGS RELEASED

393 MT

100% of scope · nil pending

SUPPLIED TILL SEP

Nil

Nil in Sep

OCT-DEC SUPPLY PLAN

360 MT

92% of scope · 120 / 120 / 120 MT

OCT-DEC ERECTION PLAN

100 MT

25% of scope · 0 erected, starts Nov-26

PEAK MONTHLY RATE (MT)

120 | 120

supply (Oct-Dec) | erection (Feb)

WORK-FRONT SEQUENCE & MONTHLY PLAN (MT)

Work front	Oct-26	Nov	Dec	Jan-27	Feb	Mar	Apr	May	Jun	Total
Foundation release	Front / drawings	Front / drawings								
Fabrication & supply	Supply	Supply	Supply	Supply						
Starter frame		Erection	Erection							
Bin support floors			Erection	Erection	Erection					
Bins / liner (TS)			TS / bins	TS / bins	TS / bins					
Handover						Handover				
Supply (MT)	120	120	120	33	—	—	—	—	—	393
Erection (MT)	—	50	50	110	120	63	—	—	—	393
Cum. erection (% of scope)	—	13%	25%	53%	84%	100%	100%	100%	100%	

KEY CONCERNS & ACTIONS

SUPPLY


Dispatch must jump from 0 MT in Sep-26 to 120 MT/month; Oct and Nov alone need 240 MT.
Action: Lock fabrication lot plan; weekly dispatch vs 120/120/120/33 MT.

ERECTION

Erection starts Nov-26 and must hold 50–120 MT/month for 5 months.
Action: Mobilise crane and erection crew before Nov-26.

INTERFACE

Bin-support and conveyor interface not yet frozen.
Action: Freeze bin-support and conveyor interface.



Supply view: Material waiting at site builds to ~260 MT by Dec-26 (supply ends 3 months before erection) - plan laydown and erection sequence.

SCOPE vs DRAWINGS vs SUPPLY vs ERECTION (MT)

Scope	393 MT
Drawings released	393 MT · 100%
Supplied till Sep	Nil
Erected till date	0 MT · starts Nov-26


Drawings complete; supply starts Oct-26; erection starts Nov-26.

Backup: combined supply and erection plan - all 3 buildings


Data as on: 30-Sep-26

Supply peaks at 870 MT/month in Dec-26; erection must climb from 50 to 538 MT/month by Feb-27 - Building structures status, MT

MONTHLY SUPPLY vs ERECTION (MT)

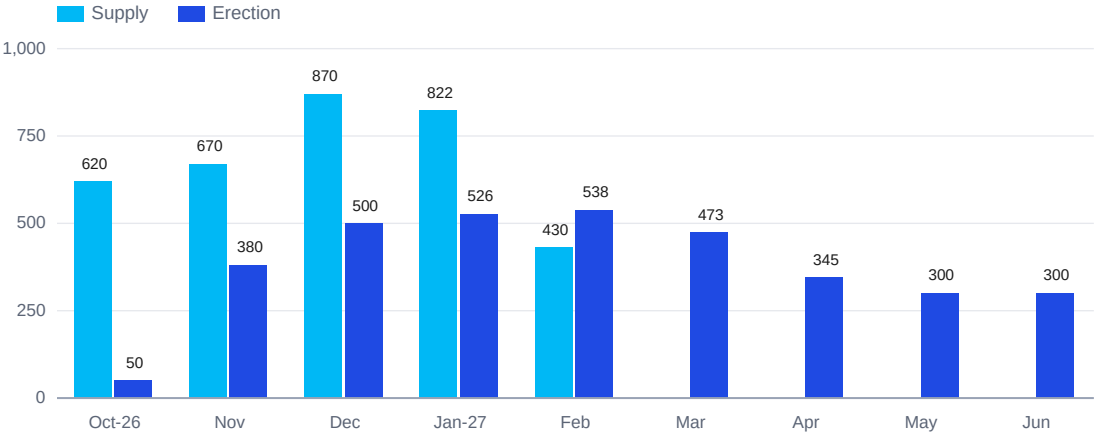

CUMULATIVE SUPPLY vs ERECTION (MT)

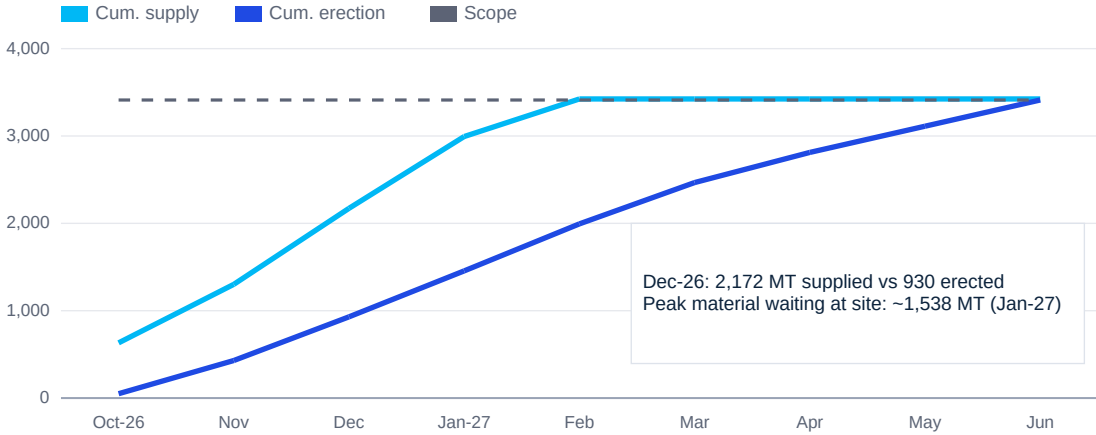

MONTHLY PLAN BY BUILDING (MT)

Oct-26–Dec shaded · – = nil

Item	Oct-26	Nov	Dec	Jan-27	Feb	Mar	Apr	May	Jun	Total
Additive Grinding Building - supply	250	300	500	520	430	–	–	–	–	2,000
Additive Grinding Building - erection	–	150	250	250	250	250	250	300	300	2,000
Screen House / Building - supply	250	250	250	269	–	–	–	–	–	1,019
Screen House / Building - erection	50	180	200	166	168	160	95	–	–	1,019
Return Fines Building - supply	120	120	120	33	–	–	–	–	–	393
Return Fines Building - erection	–	50	50	110	120	63	–	–	–	393
Total supply	620	670	870	822	430	–	–	–	–	3,412
Total erection	50	380	500	526	538	473	345	300	300	3,412

GAPS TO CLOSE BEFORE PLAN SIGN-OFF

- Additive Grinding Building: Only 1,399 of 2,000 MT drawings released; 601 MT (30%) pending. Cumulative supply crosses 1,399 MT in Jan-27.
- Additive Grinding Building: Oct-26–Feb supply plan totals 2,000 MT but the balance is 1,988 MT (12 MT already done) - quantities not reconciled against scope.
- Additive Grinding Building: Dispatch must jump from 12 MT in Sep-26 to 520 MT/month; Dec and Jan-27 alone need 1,020 MT.
- Screen House / Building: Dispatch must jump from 0 MT in Sep-26 to 269 MT/month; Oct and Jan-27 alone need 519 MT.

Material waiting at site = cumulative supply - cumulative erection. Plan laydown for the peak, and size erection crews to the monthly erection rate.
