

Monthly Progress Summary

Planned %

75.9%

Actual %

57.3%

Variance

-18.6%

Forecast finish

17-May-27

Completed

61 / 116

In progress

20

Late start

8


Overdue

9


Critical

5

S-curve - cumulative progress (duration weighted)

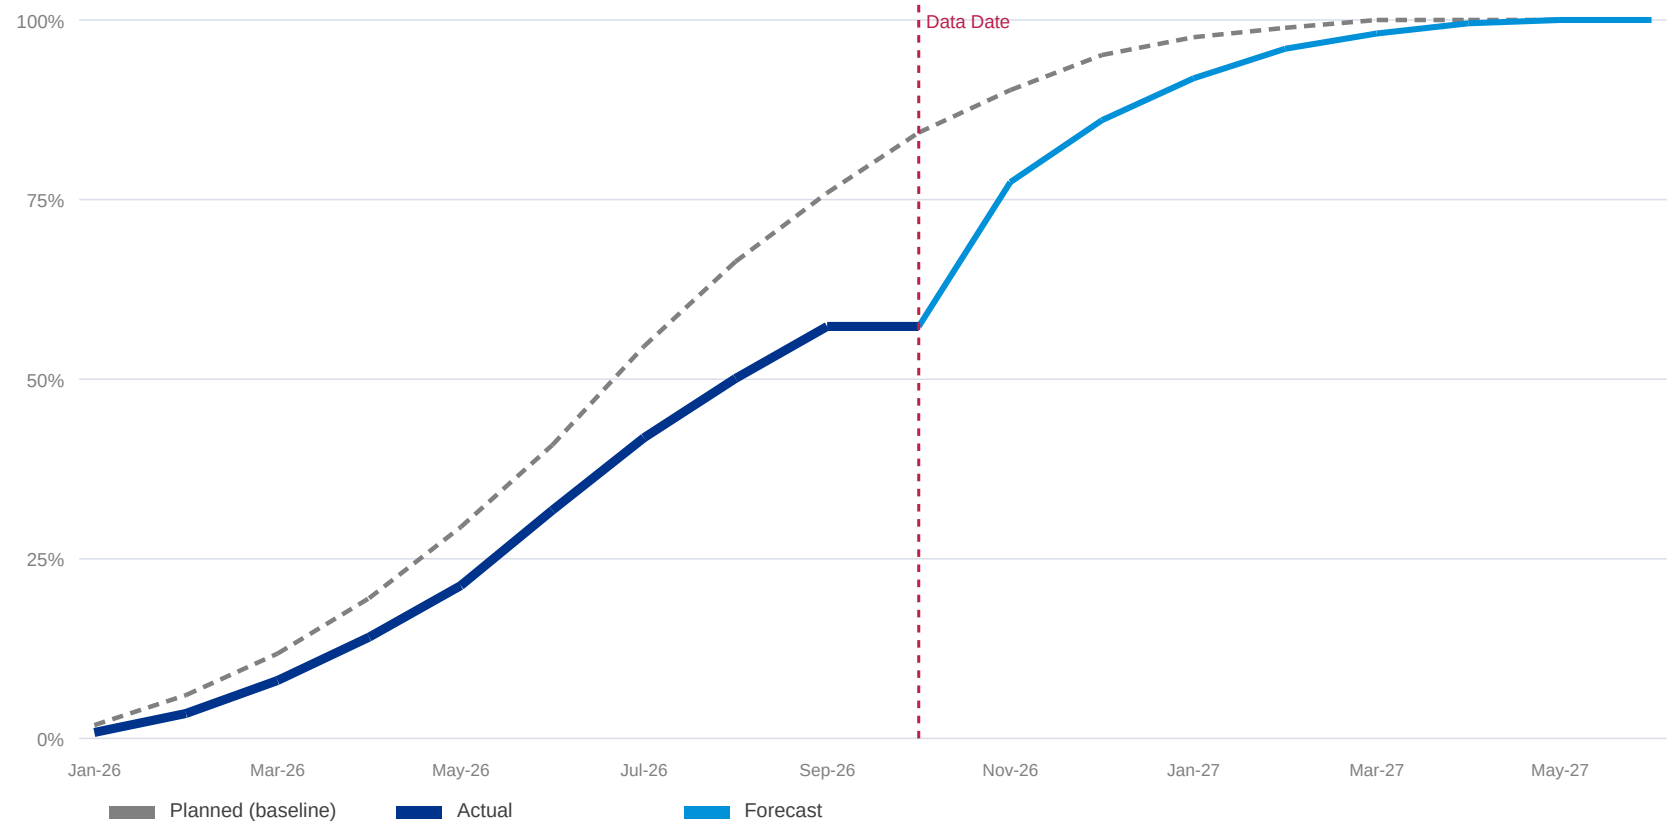

Building-wise progress (planned vs actual)

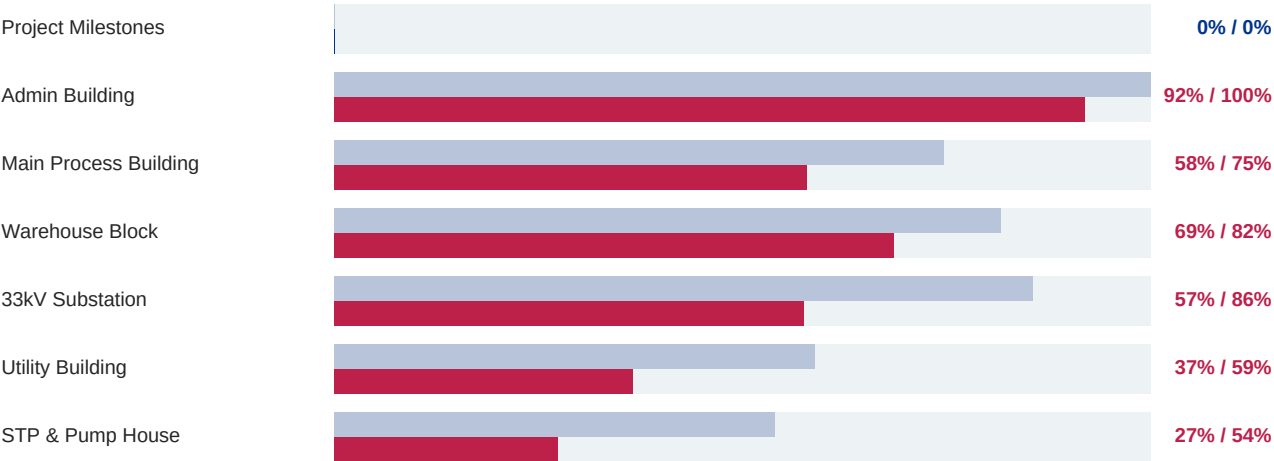

EPC-wise progress

EPC	Activities	Planned %	Actual %	Variance	Late start	Overdue
Engineering	24	100.0	99.2	-0.8	0	2
Procurement	24	85.2	59.3	-25.9	3	3
Construction	66	63.1	42.5	-20.6	5	4
Others	2	0.0	0.0	+0.0	0	0

Engine insights

- Overall progress is 57.3% against a planned 75.9% as of 01-Oct-2026 (-18.6%). Progress gained this period: 4.4%.
- 8 activities were due to start before the Data Date but have not started.
- 9 activities are past their finish date and still open.
- 2 future activities show progress - check these were really started early.
- 16 activities still need your update this month.
- 2 activities are progressing out of sequence.
- 33kV Substation is the most behind: 57.5% vs 85.6% planned (-28.1%).
- EPC progress: Engineering 99%, Procurement 59%, Construction 42%.
- Forecast project finish: 17-May-2027 - 41 working days later than baseline.
- 7 milestones are forecast late; worst: ADM-C1190 Building handover to client (11-Sep-26 -> 10-Nov-26).
- 5 activities are critical. Watch them in the look-ahead.

Gantt layout (1/3)

Activity ID	Activity Name	OD	RD	%	Start	Finish	TF	2026												2027					
								J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J
Industrial Plant Expansion - Phase 2 (Demo)		417		57%	05-Jan-26	17-May-27	0																		
Project Milestones		417		0%	05-Jan-26	17-May-27	0																		
MS-1000	Notice to proceed / Project start	0	0	100%	05-Jan-26 A	05-Jan-26 A		◆ Notice to proceed / Project start																	
MS-9000	Plant mechanical completion	0	0	0%	17-May-27	17-May-27	0													◆ Plant mechanical comple...					
Admin Building		256		92%	08-Jan-26	10-Nov-26	158																		
Engineering		80		100%	08-Jan-26	14-Apr-26																			
ADM-E1010	Design basis & architectural layout	19	0	100%	08-Jan-26 A	10-Feb-26 A																			
ADM-E1020	Structural design & IFC drawings	34	0	100%	21-Jan-26 A	20-Mar-26 A																			
ADM-E1030	MEP design & drawings	36	0	100%	17-Feb-26 A	14-Apr-26 A																			
ADM-E1040	Drawing approval by client	10	0	100%	24-Mar-26 A	14-Apr-26 A																			
Procurement		110		100%	25-Mar-26	31-Jul-26																			
ADM-P1050	Structural steel - PO placement	11	0	100%	25-Mar-26 A	07-Apr-26 A																			
ADM-P1060	Structural steel - fabrication & supply to site	58	0	100%	13-Apr-26 A	01-Jul-26 A																			
ADM-P1070	MEP equipment - PO placement	13	0	100%	15-Apr-26 A	28-Apr-26 A																			
ADM-P1080	MEP equipment - manufacturing & delivery	70	0	100%	04-May-26 A	31-Jul-26 A																			
Construction		256		85%	08-Jan-26	10-Nov-26	158																		
ADM-C1090	Site mobilisation & survey	5	0	100%	08-Jan-26 A	14-Jan-26 A																			
ADM-C1100	Excavation	17	0	100%	04-Feb-26 A	26-Feb-26 A																			
ADM-C1110	PCC & foundation concreting	30	0	100%	14-Feb-26 A	26-Mar-26 A																			
ADM-C1120	Plinth beam & backfilling	20	0	100%	28-Mar-26 A	23-Apr-26 A																			
ADM-C1130	Superstructure - RCC / steel erection	54	0	100%	01-May-26 A	13-Jul-26 A																			
ADM-C1150	Masonry & plastering	37	0	100%	29-May-26 A	11-Jul-26 A																			
ADM-C1140	Roofing & cladding	21	0	100%	13-Jul-26 A	03-Aug-26 A																			
ADM-C1160	MEP installation	48	18	62%	04-Aug-26 A	23-Oct-26	158																		
ADM-C1170	Finishes - flooring & painting	40	11	73%	05-Aug-26 A	14-Oct-26	179																		
ADM-C1180	Testing & commissioning	14	14	0%	24-Oct-26	10-Nov-26	158																		
ADM-C1190	Building handover to client	0	0	0%	10-Nov-26	10-Nov-26	158													◆ Building handover to client					
Main Process Building		400		58%	24-Jan-26	17-May-27	0																		
Engineering		141		100%	30-Jan-26	15-Jul-26																			
MPB-E1010	Design basis & architectural layout	32	0	100%	30-Jan-26 A	20-Mar-26 A																			
MPB-E1020	Structural design & IFC drawings	52	0	100%	11-Feb-26 A	04-May-26 A																			
MPB-E1030	MEP design & drawings	67	0	100%	30-Mar-26 A	15-Jul-26 A																			
MPB-E1040	Drawing approval by client	21	0	100%	22-May-26 A	15-Jul-26 A																			
Procurement		213		59%	11-May-26	19-Jan-27	0																		
MPB-P1050	Structural steel - PO placement	22	0	100%	11-May-26 A	09-Jun-26 A																			
MPB-P1060	Structural steel - fabrication & supply to site	99	18	82%	15-Jun-26 A	23-Oct-26	34																		
MPB-P1070	MEP equipment - PO placement	22	0	100%	20-Jul-26 A	13-Aug-26 A																			
MPB-P1080	MEP equipment - manufacturing & delivery	124	91	27%	18-Aug-26 A	19-Jan-27	0																		
Construction		400		42%	24-Jan-26	17-May-27	0																		
MPB-C1090	Site mobilisation & survey	10	0	100%	24-Jan-26 A	06-Feb-26 A																			
MPB-C1100	Excavation	32	0	100%	28-Feb-26 A	09-Apr-26 A																			
MPB-C1110	PCC & foundation concreting	45	0	100%	18-Mar-26 A	12-May-26 A																			
MPB-C1120	Plinth beam & backfilling	28	0	100%	22-May-26 A	26-Jun-26 A																			
MPB-C1130	Superstructure - RCC / steel erection	102	49	52%	08-Jul-26 A	30-Nov-26	49																		
MPB-C1150	Masonry & plastering	69	35	49%	06-Aug-26 A	13-Nov-26	81																		
MPB-C1140	Roofing & cladding	39	39	0%	25-Nov-26	09-Jan-27	49																		
MPB-C1170	Finishes - flooring & painting	58	58	0%	11-Jan-27	19-Mar-27	49																		
MPB-C1160	MEP installation	78	78	0%	20-Jan-27	22-Apr-27	0																		
MPB-C1180	Testing & commissioning	21	21	0%	23-Apr-27	17-May-27	0																		
MPB-C1190	Building handover to client	0	0	0%	17-May-27	17-May-27	0													◆ Building handover to client					
Warehouse Block		295		69%	27-Feb-26	15-Feb-27	77																		
Engineering		83		100%	06-Mar-26	11-Jun-26																			
WHS-E1010	Design basis & architectural layout	21	0	100%	06-Mar-26 A	08-Apr-26 A																			
WHS-E1020	Structural design & IFC drawings	30	0	100%	18-Mar-26 A	06-May-26 A																			
WHS-E1030	MEP design & drawings	42	0	100%	15-Apr-26 A	11-Jun-26 A																			
WHS-E1040	Drawing approval by client	14	0	100%	15-May-26 A	11-Jun-26 A																			

Gantt layout (2/3)

Activity ID	Activity Name	OD	RD	%	Start	Finish	TF	2026												2027							
								J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	
Procurement		157		82%	07-May-26	10-Nov-26	77																				
WHS-P1050	Structural steel - PO placement	13	0	100%	07-May-26 A	21-May-26 A																					
WHS-P1060	Structural steel - fabrication & supply to site	58	0	100%	28-May-26 A	05-Aug-26 A																					
WHS-P1070	MEP equipment - PO placement	18	0	100%	13-Jun-26 A	08-Jul-26 A																					
WHS-P1080	MEP equipment - manufacturing & delivery	83	32	62%	09-Jul-26 A	10-Nov-26	77																				
Construction		295		52%	27-Feb-26	15-Feb-27	77																				
WHS-C1090	Site mobilisation & survey	8	0	100%	27-Feb-26 A	09-Mar-26 A																					
WHS-C1100	Excavation	19	0	100%	30-Mar-26 A	24-Apr-26 A																					
WHS-C1110	PCC & foundation concreting	37	0	100%	13-Apr-26 A	25-May-26 A																					
WHS-C1120	Plinth beam & backfilling	20	0	100%	28-May-26 A	22-Jun-26 A																					
WHS-C1130	Superstructure - RCC / steel erection	66	1	99%	24-Jun-26 A	01-Oct-26	79																				
WHS-C1150	Masonry & plastering	41	9	77%	23-Jul-26 A	12-Oct-26	99																				
WHS-C1140	Roofing & cladding	32	32	0%	01-Oct-26	10-Nov-26	116																				
WHS-C1160	MEP installation	63	63	0%	11-Nov-26	23-Jan-27	77																				
WHS-C1170	Finishes - flooring & painting	42	42	0%	11-Nov-26	30-Dec-26	116																				
WHS-C1180	Testing & commissioning	18	18	0%	25-Jan-27	15-Feb-27	77																				
WHS-C1190	Building handover to client	0	0	0%	15-Feb-27	15-Feb-27	77	Building handover to client																			
33kV Substation		253		57%	27-Mar-26	22-Jan-27	83																				
Engineering		76		100%	10-Apr-26	07-Jul-26																					
SUB-E1010	Design basis & architectural layout	20	0	100%	10-Apr-26 A	13-May-26 A																					
SUB-E1020	Structural design & IFC drawings	26	0	100%	27-Apr-26 A	01-Jun-26 A																					
SUB-E1030	MEP design & drawings	35	0	100%	22-May-26 A	07-Jul-26 A																					
SUB-E1040	Drawing approval by client	12	0	100%	12-Jun-26 A	07-Jul-26 A																					
Procurement		128		78%	10-Jun-26	10-Nov-26	83																				
SUB-P1050	Structural steel - PO placement	12	0	100%	10-Jun-26 A	23-Jun-26 A																					
SUB-P1060	Structural steel - fabrication & supply to site	59	1	98%	01-Jul-26 A	01-Oct-26	83																				
SUB-P1070	MEP equipment - PO placement	15	0	100%	14-Jul-26 A	29-Jul-26 A																					
SUB-P1080	MEP equipment - manufacturing & delivery	62	32	49%	07-Aug-26 A	10-Nov-26	96																				
Construction		253		33%	27-Mar-26	22-Jan-27	96																				
SUB-C1090	Site mobilisation & survey	5	0	100%	27-Mar-26 A	01-Apr-26 A																					
SUB-C1100	Excavation	18	0	100%	15-May-26 A	09-Jun-26 A																					
SUB-C1110	PCC & foundation concreting	29	0	100%	03-Jun-26 A	09-Jul-26 A																					
SUB-C1120	Plinth beam & backfilling	17	0	100%	21-Jul-26 A	08-Aug-26 A																					
SUB-C1130	Superstructure - RCC / steel erection	53	31	41%	19-Aug-26 A	07-Nov-26	98																				
SUB-C1150	Masonry & plastering	32	32	0%	01-Oct-26	10-Nov-26	118																				
SUB-C1140	Roofing & cladding	23	23	0%	03-Nov-26	30-Nov-26	101																				
SUB-C1160	MEP installation	48	48	0%	11-Nov-26	06-Jan-27	96																				
SUB-C1170	Finishes - flooring & painting	40	40	0%	01-Dec-26	16-Jan-27	101																				
SUB-C1180	Testing & commissioning	14	14	0%	07-Jan-27	22-Jan-27	96																				
SUB-C1190	Building handover to client	0	0	0%	22-Jan-27	22-Jan-27	96	Building handover to client																			
Utility Building		314		37%	25-Apr-26	04-May-27	11																				
Engineering		78		100%	14-May-26	12-Aug-26																					
UTL-E1010	Design basis & architectural layout	24	0	100%	14-May-26 A	15-Jun-26 A																					
UTL-E1020	Structural design & IFC drawings	35	0	100%	22-May-26 A	16-Jul-26 A																					
UTL-E1030	MEP design & drawings	38	0	100%	24-Jun-26 A	12-Aug-26 A																					
UTL-E1040	Drawing approval by client	13	0	100%	28-Jul-26 A	12-Aug-26 A																					
Procurement		169		21%	17-Jul-26	05-Feb-27	11																				
UTL-P1050	Structural steel - PO placement	14	0	100%	17-Jul-26 A	03-Aug-26 A																					
UTL-P1060	Structural steel - fabrication & supply to site	61	54	29%	04-Aug-26 A	05-Dec-26	46																				
UTL-P1070	MEP equipment - PO placement	17	12	44%	20-Aug-26 A	15-Oct-26	11																				
UTL-P1080	MEP equipment - manufacturing & delivery	93	93	0%	16-Oct-26	05-Feb-27	11																				
Construction		314		24%	25-Apr-26	04-May-27	11																				
UTL-C1090	Site mobilisation & survey	7	0	100%	25-Apr-26 A	02-May-26 A																					
UTL-C1100	Excavation	24	0	100%	04-Jun-26 A	01-Jul-26 A																					
UTL-C1110	PCC & foundation concreting	30	0	100%	16-Jun-26 A	27-Jul-26 A																					
UTL-C1120	Plinth beam & backfilling	21	0	100%	03-Aug-26 A	27-Aug-26 A																					

Actual work

Remaining work

Critical remaining

Baseline

Milestone

Data Date

Late start

Overdue

Future progress

Invalid

Gantt layout (3/3)

Activity ID	Activity Name	OD	RD	%	Start	Finish	TF	2026												2027								
								J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J		
UTL-C1130	Superstructure - RCC / steel erection	69	69	0%	01-Oct-26	23-Dec-26	61																					
UTL-C1150	Masonry & plastering	47	47	0%	27-Oct-26	21-Dec-26	86																					
UTL-C1140	Roofing & cladding	29	29	0%	18-Dec-26	21-Jan-27	61																					
UTL-C1170	Finishes - flooring & painting	36	36	0%	22-Jan-27	05-Mar-27	61																					
UTL-C1160	MEP installation	59	59	0%	06-Feb-27	16-Apr-27	11																					
UTL-C1180	Testing & commissioning	15	15	0%	17-Apr-27	04-May-27	11																					
UTL-C1190	Building handover to client	0	0	0%	04-May-27	04-May-27	11																					
STP & Pump House		234		27%	29-May-26	04-Mar-27	51																					
Engineering		84		93%	02-Jul-26	09-Oct-26	51																					
STP-E1010	Design basis & architectural layout	14	0	100%	02-Jul-26 A	23-Jul-26 A																						
STP-E1020	Structural design & IFC drawings	21	0	100%	10-Jul-26 A	11-Aug-26 A																						
STP-E1030	MEP design & drawings	29	6	84%	29-Jul-26 A	09-Oct-26	51																					
STP-E1040	Drawing approval by client	9	1	95%	12-Aug-26 A	09-Oct-26	151																					
Procurement		114		9%	14-Aug-26	30-Dec-26	62																					
STP-P1050	Structural steel - PO placement	9	0	100%	14-Aug-26 A	25-Aug-26 A																						
STP-P1060	Structural steel - fabrication & supply to site	40	42	5%	29-Aug-26 A	21-Nov-26	87																					
STP-P1070	MEP equipment - PO placement	11	11	0%	10-Oct-26	23-Oct-26	62																					
STP-P1080	MEP equipment - manufacturing & delivery	56	56	0%	24-Oct-26	30-Dec-26	62																					
Construction		234		16%	29-May-26	04-Mar-27	62																					
STP-C1090	Site mobilisation & survey	5	0	100%	29-May-26 A	03-Jun-26 A																						
STP-C1100	Excavation	15	0	100%	24-Jul-26 A	10-Aug-26 A																						
STP-C1110	PCC & foundation concreting	28	15	58%	06-Aug-26 A	19-Oct-26	72																					
STP-C1150	Masonry & plastering	33	31	5%	26-Aug-26 A	07-Jan-27	76																					
STP-C1160	MEP installation	43	41	5%	26-Aug-26 A	17-Feb-27	62																					
STP-C1120	Plinth beam & backfilling	15	15	0%	21-Oct-26	06-Nov-26	72																					
STP-C1130	Superstructure - RCC / steel erection	43	43	0%	07-Nov-26	29-Dec-26	72																					
STP-C1140	Roofing & cladding	20	20	0%	23-Dec-26	15-Jan-27	72																					
STP-C1170	Finishes - flooring & painting	30	30	0%	16-Jan-27	20-Feb-27	72																					
STP-C1180	Testing & commissioning	13	13	0%	18-Feb-27	04-Mar-27	62																					
STP-C1190	Building handover to client	0	0	0%	04-Mar-27	04-Mar-27	62																					

Activities needing attention

Flag	Activity ID	Activity Name	Building	EPC	Status	Ref Start	Ref Finish	Start	Finish	%	TF
Overdue	ADM-C1170	Finishes - flooring & painting	Admin Building	Construction	In Progress	05-Aug-26	28-Sep-26	05-Aug-26	14-Oct-26	73%	179
Overdue	WHS-C1130	Superstructure - RCC / steel erection	Warehouse Block	Construction	In Progress	24-Jun-26	10-Sep-26	24-Jun-26	01-Oct-26	99%	79
Late start	WHS-C1140	Roofing & cladding	Warehouse Block	Construction	Not Started	05-Sep-26	13-Oct-26	01-Oct-26	10-Nov-26	0%	116
Overdue	WHS-C1150	Masonry & plastering	Warehouse Block	Construction	In Progress	23-Jul-26	22-Sep-26	23-Jul-26	12-Oct-26	77%	99
Overdue	SUB-P1060	Structural steel - fabrication & supply to site	33kV Substation	Procurement	In Progress	01-Jul-26	17-Sep-26	01-Jul-26	01-Oct-26	98%	83
Late start	SUB-C1150	Masonry & plastering	33kV Substation	Construction	Not Started	11-Sep-26	19-Oct-26	01-Oct-26	10-Nov-26	0%	118
Overdue	UTL-P1070	MEP equipment - PO placement	Utility Building	Procurement	In Progress	20-Aug-26	14-Sep-26	20-Aug-26	15-Oct-26	44%	11
Late start	UTL-P1080	MEP equipment - manufacturing & delivery	Utility Building	Procurement	Not Started	15-Sep-26	05-Jan-27	16-Oct-26	05-Feb-27	0%	11
Late start	UTL-C1130	Superstructure - RCC / steel erection	Utility Building	Construction	Not Started	01-Sep-26	23-Nov-26	01-Oct-26	23-Dec-26	0%	61
Late start	UTL-C1150	Masonry & plastering	Utility Building	Construction	Not Started	24-Sep-26	20-Nov-26	27-Oct-26	21-Dec-26	0%	86
Overdue	STP-E1030	MEP design & drawings	STP & Pump House	Engineering	In Progress	29-Jul-26	08-Sep-26	29-Jul-26	09-Oct-26	84%	51
Overdue	STP-E1040	Drawing approval by client	STP & Pump House	Engineering	In Progress	12-Aug-26	08-Sep-26	12-Aug-26	09-Oct-26	95%	151
Overdue	STP-P1070	MEP equipment - PO placement	STP & Pump House	Procurement	Not Started	09-Sep-26	21-Sep-26	10-Oct-26	23-Oct-26	0%	62
Late start	STP-P1070	MEP equipment - PO placement	STP & Pump House	Procurement	Not Started	09-Sep-26	21-Sep-26	10-Oct-26	23-Oct-26	0%	62
Late start	STP-P1080	MEP equipment - manufacturing & delivery	STP & Pump House	Procurement	Not Started	22-Sep-26	28-Nov-26	24-Oct-26	30-Dec-26	0%	62
Overdue	STP-C1110	PCC & foundation concreting	STP & Pump House	Construction	In Progress	06-Aug-26	17-Sep-26	06-Aug-26	19-Oct-26	58%	72
Late start	STP-C1120	Plinth beam & backfilling	STP & Pump House	Construction	Not Started	18-Sep-26	06-Oct-26	21-Oct-26	06-Nov-26	0%	72
Future progress	STP-C1150	Masonry & plastering	STP & Pump House	Construction	In Progress	26-Aug-26	07-Dec-26	26-Aug-26	07-Jan-27	5%	76
Out of sequence	STP-C1150	Masonry & plastering	STP & Pump House	Construction	In Progress	26-Aug-26	07-Dec-26	26-Aug-26	07-Jan-27	5%	76
Future progress	STP-C1160	MEP installation	STP & Pump House	Construction	In Progress	26-Aug-26	16-Jan-27	26-Aug-26	17-Feb-27	5%	62
Out of sequence	STP-C1160	MEP installation	STP & Pump House	Construction	In Progress	26-Aug-26	16-Jan-27	26-Aug-26	17-Feb-27	5%	62

4-week look-ahead from 01-Oct-2026

Activity ID	Activity Name	Building	EPC	Status	Start	Finish	Rem Dur	%	TF
MPB-P1060	Structural steel - fabrication & supply to site	Main Process Building	Procurement	In Progress	15-Jun-26	23-Oct-26	18	82%	34
WHS-C1130	Superstructure - RCC / steel erection	Warehouse Block	Construction	In Progress	24-Jun-26	01-Oct-26	1	99%	79
SUB-P1060	Structural steel - fabrication & supply to site	33kV Substation	Procurement	In Progress	01-Jul-26	01-Oct-26	1	98%	83
MPB-C1130	Superstructure - RCC / steel erection	Main Process Building	Construction	In Progress	08-Jul-26	30-Nov-26	49	52%	49
WHS-P1080	MEP equipment - manufacturing & delivery	Warehouse Block	Procurement	In Progress	09-Jul-26	10-Nov-26	32	62%	77
WHS-C1150	Masonry & plastering	Warehouse Block	Construction	In Progress	23-Jul-26	12-Oct-26	9	77%	99
STP-E1030	MEP design & drawings	STP & Pump House	Engineering	In Progress	29-Jul-26	09-Oct-26	6	84%	51
ADM-C1160	MEP installation	Admin Building	Construction	In Progress	04-Aug-26	23-Oct-26	18	62%	158
UTL-P1060	Structural steel - fabrication & supply to site	Utility Building	Procurement	In Progress	04-Aug-26	05-Dec-26	54	29%	46
ADM-C1170	Finishes - flooring & painting	Admin Building	Construction	In Progress	05-Aug-26	14-Oct-26	11	73%	179
MPB-C1150	Masonry & plastering	Main Process Building	Construction	In Progress	06-Aug-26	13-Nov-26	35	49%	81
STP-C1110	PCC & foundation concreting	STP & Pump House	Construction	In Progress	06-Aug-26	19-Oct-26	15	58%	72
SUB-P1080	MEP equipment - manufacturing & delivery	33kV Substation	Procurement	In Progress	07-Aug-26	10-Nov-26	32	49%	96
STP-E1040	Drawing approval by client	STP & Pump House	Engineering	In Progress	12-Aug-26	09-Oct-26	1	95%	151
MPB-P1080	MEP equipment - manufacturing & delivery	Main Process Building	Procurement	In Progress	18-Aug-26	19-Jan-27	91	27%	0
SUB-C1130	Superstructure - RCC / steel erection	33kV Substation	Construction	In Progress	19-Aug-26	07-Nov-26	31	41%	98
UTL-P1070	MEP equipment - PO placement	Utility Building	Procurement	In Progress	20-Aug-26	15-Oct-26	12	44%	11
STP-C1150	Masonry & plastering	STP & Pump House	Construction	In Progress	26-Aug-26	07-Jan-27	31	5%	76
STP-C1160	MEP installation	STP & Pump House	Construction	In Progress	26-Aug-26	17-Feb-27	41	5%	62
STP-P1060	Structural steel - fabrication & supply to site	STP & Pump House	Procurement	In Progress	29-Aug-26	21-Nov-26	42	5%	87
SUB-C1150	Masonry & plastering	33kV Substation	Construction	Not Started	01-Oct-26	10-Nov-26	32	0%	118
UTL-C1130	Superstructure - RCC / steel erection	Utility Building	Construction	Not Started	01-Oct-26	23-Dec-26	69	0%	61
WHS-C1140	Roofing & cladding	Warehouse Block	Construction	Not Started	01-Oct-26	10-Nov-26	32	0%	116
STP-P1070	MEP equipment - PO placement	STP & Pump House	Procurement	Not Started	10-Oct-26	23-Oct-26	11	0%	62
UTL-P1080	MEP equipment - manufacturing & delivery	Utility Building	Procurement	Not Started	16-Oct-26	05-Feb-27	93	0%	11
STP-C1120	Plinth beam & backfilling	STP & Pump House	Construction	Not Started	21-Oct-26	06-Nov-26	15	0%	72
ADM-C1180	Testing & commissioning	Admin Building	Construction	Not Started	24-Oct-26	10-Nov-26	14	0%	158
STP-P1080	MEP equipment - manufacturing & delivery	STP & Pump House	Procurement	Not Started	24-Oct-26	30-Dec-26	56	0%	62
UTL-C1150	Masonry & plastering	Utility Building	Construction	Not Started	27-Oct-26	21-Dec-26	47	0%	86

Schedule health check - score 46%

Check	Result	Count	Of	%	Guideline
Missing logic (open ends)	PASS	0	55	0.0	Activities without a predecessor or a successor (first/last milestones excepted). Target <= 5%.
Leads (negative lags)	FAIL	6	156	3.8	Relationships with a negative lag hide logic. Target 0.
Positive lags	FAIL	46	156	29.5	Lags should be replaced with activities where possible. Target <= 5%.
Relationship types (FS >= 90%)	FAIL	48	156	69.2	Finish-to-Start should dominate. Shows the share of FS links.
Hard constraints	PASS	0	55	0.0	Must/finish-on or before constraints block logic. Target <= 5%.
High float (> 44 days)	FAIL	44	55	80.0	Usually means missing successors. Target <= 5%.
Negative float	PASS	0	55	0.0	Project is late against a constraint / must-finish date. Target 0.
High duration (> 44 days)	FAIL	20	55	36.4	Break long activities down for better control. Target <= 5%.
Invalid dates	PASS	0	116	0.0	Actuals after the Data Date or forecasts before it. Target 0.
Missed activities (finished late vs baseline)	FAIL	82	84	97.6	Planned to finish by the Data Date but finished late or not at all. Target <= 5%.
Critical path exists	PASS	5	55	9.1	A continuous critical path should drive the finish.
Baseline Execution Index (BEI >= 0.95)	FAIL	61	84	72.6	Activities completed / activities that should have been completed. 0.73
Logic loops	PASS	0	116	0.0	No circular logic.
