

Monthly Progress Summary

Planned %

75.9%

Actual %

57.3%

Variance

-18.6%

Forecast finish

17-May-27

Completed

61 / 116

In progress

20

Late start

8


Overdue

9


Critical

5

S-curve - cumulative progress (duration weighted)

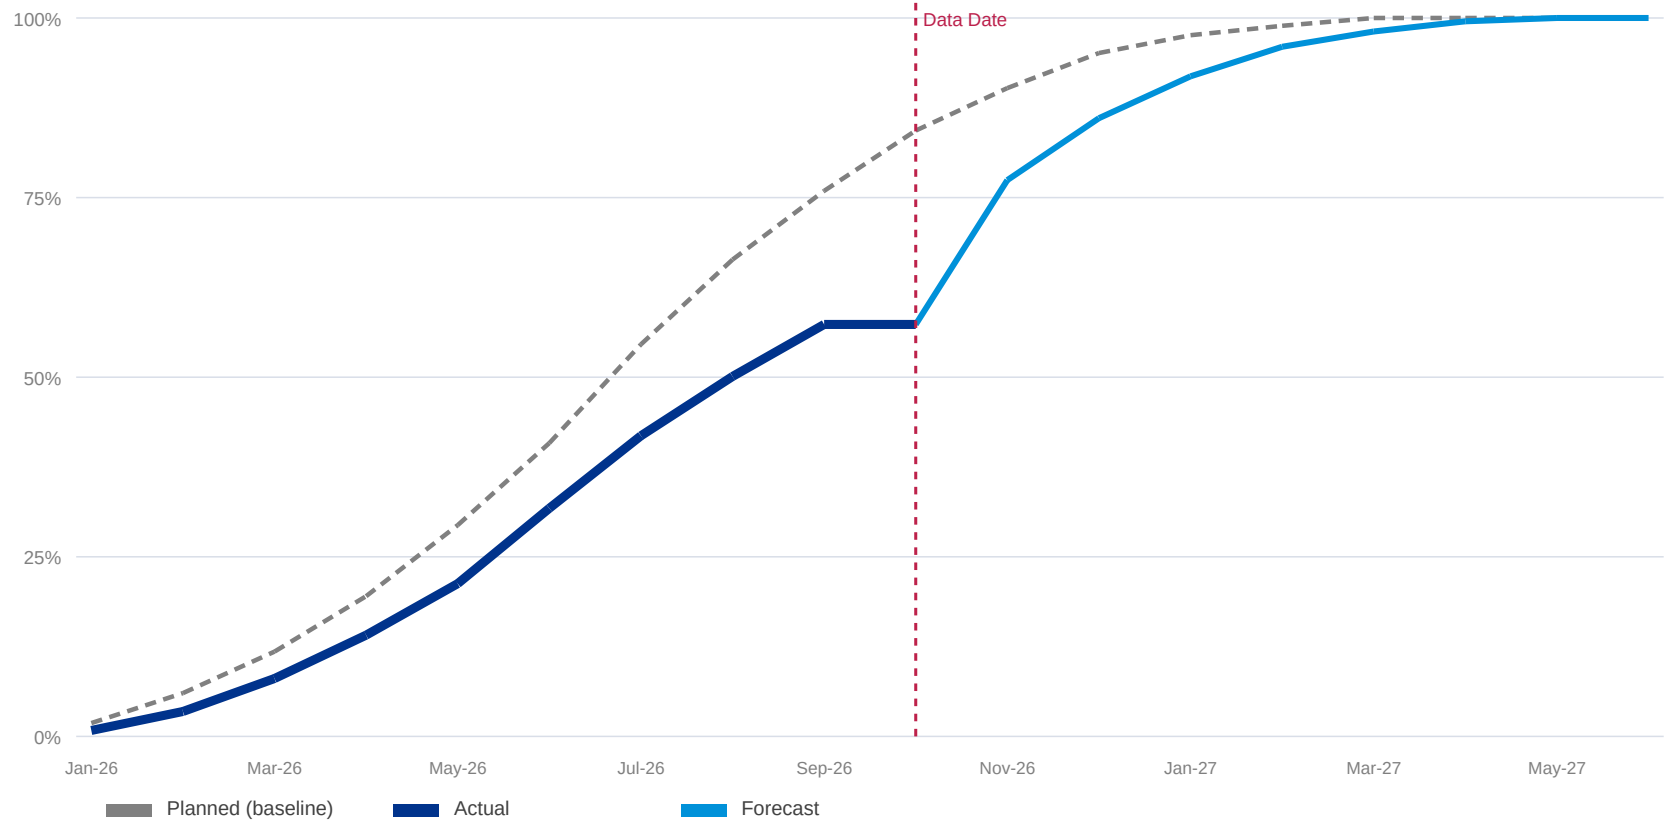

Building-wise progress (planned vs actual)

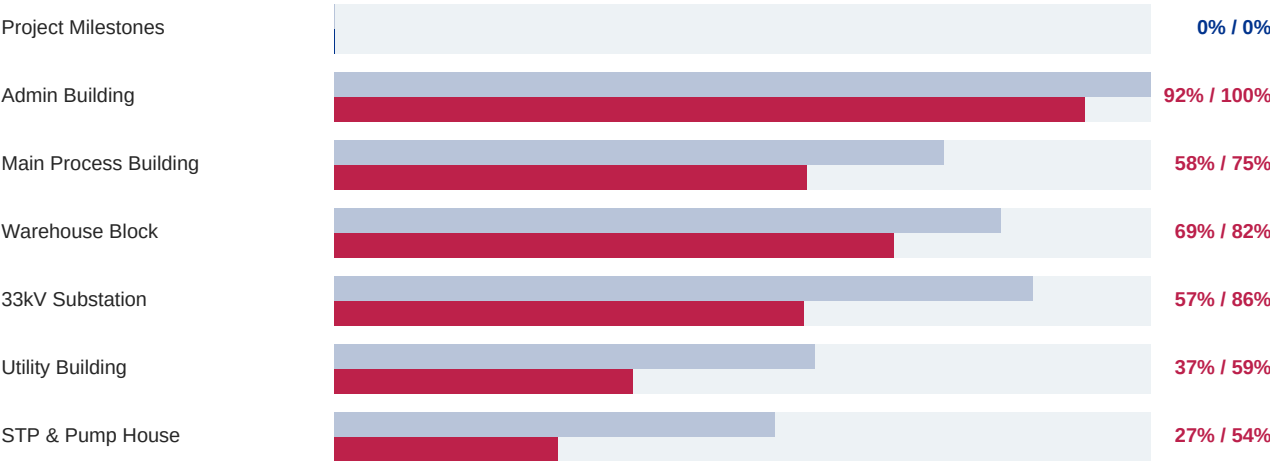

EPC-wise progress

EPC	Activities	Planned %	Actual %	Variance	Late start	Overdue
Engineering	24	100.0	99.2	-0.8	0	2
Procurement	24	85.2	59.3	-25.9	3	3
Construction	66	63.1	42.5	-20.6	5	4
Others	2	0.0	0.0	+0.0	0	0

Engine insights

- Overall progress is 57.3% against a planned 75.9% as of 01-Oct-2026 (-18.6%). Progress gained this period: 4.4%.
- 8 activities were due to start before the Data Date but have not started.
- 9 activities are past their finish date and still open.
- 2 future activities show progress - check these were really started early.
- 16 activities still need your update this month.
- 2 activities are progressing out of sequence.
- 33kV Substation is the most behind: 57.5% vs 85.6% planned (-28.1%).
- EPC progress: Engineering 99%, Procurement 59%, Construction 42%.
- Forecast project finish: 17-May-2027 - 41 working days later than baseline.
- 7 milestones are forecast late; worst: ADM-C1190 Building handover to client (11-Sep-26 -> 10-Nov-26).
- 5 activities are critical. Watch them in the look-ahead.

Gantt layout (2/3)

Activity ID	Activity Name	OD	RD	%	Start	Finish	TF	2026												2027							
								J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	
Procurement		157		82%	07-May-26	10-Nov-26	77																				
WHS-P1050	Structural steel - PO placement	13	0	100%	07-May-26 A	21-May-26 A																					
WHS-P1060	Structural steel - fabrication & supply to site	58	0	100%	28-May-26 A	05-Aug-26 A																					
WHS-P1070	MEP equipment - PO placement	18	0	100%	13-Jun-26 A	08-Jul-26 A																					
WHS-P1080	MEP equipment - manufacturing & delivery	83	32	62%	09-Jul-26 A	10-Nov-26	77																				
Construction		295		52%	27-Feb-26	15-Feb-27	77																				
WHS-C1090	Site mobilisation & survey	8	0	100%	27-Feb-26 A	09-Mar-26 A																					
WHS-C1100	Excavation	19	0	100%	30-Mar-26 A	24-Apr-26 A																					
WHS-C1110	PCC & foundation concreting	37	0	100%	13-Apr-26 A	25-May-26 A																					
WHS-C1120	Plinth beam & backfilling	20	0	100%	28-May-26 A	22-Jun-26 A																					
WHS-C1130	Superstructure - RCC / steel erection	66	1	99%	24-Jun-26 A	01-Oct-26	79																				
WHS-C1150	Masonry & plastering	41	9	77%	23-Jul-26 A	12-Oct-26	99																				
WHS-C1140	Roofing & cladding	32	32	0%	01-Oct-26	10-Nov-26	116																				
WHS-C1160	MEP installation	63	63	0%	11-Nov-26	23-Jan-27	77																				
WHS-C1170	Finishes - flooring & painting	42	42	0%	11-Nov-26	30-Dec-26	116																				
WHS-C1180	Testing & commissioning	18	18	0%	25-Jan-27	15-Feb-27	77																				
WHS-C1190	Building handover to client	0	0	0%	15-Feb-27	15-Feb-27	77	Building handover to client																			
33kV Substation		253		57%	27-Mar-26	22-Jan-27	83																				
Engineering		76		100%	10-Apr-26	07-Jul-26																					
SUB-E1010	Design basis & architectural layout	20	0	100%	10-Apr-26 A	13-May-26 A																					
SUB-E1020	Structural design & IFC drawings	26	0	100%	27-Apr-26 A	01-Jun-26 A																					
SUB-E1030	MEP design & drawings	35	0	100%	22-May-26 A	07-Jul-26 A																					
SUB-E1040	Drawing approval by client	12	0	100%	12-Jun-26 A	07-Jul-26 A																					
Procurement		128		78%	10-Jun-26	10-Nov-26	83																				
SUB-P1050	Structural steel - PO placement	12	0	100%	10-Jun-26 A	23-Jun-26 A																					
SUB-P1060	Structural steel - fabrication & supply to site	59	1	98%	01-Jul-26 A	01-Oct-26	83																				
SUB-P1070	MEP equipment - PO placement	15	0	100%	14-Jul-26 A	29-Jul-26 A																					
SUB-P1080	MEP equipment - manufacturing & delivery	62	32	49%	07-Aug-26 A	10-Nov-26	96																				
Construction		253		33%	27-Mar-26	22-Jan-27	96																				
SUB-C1090	Site mobilisation & survey	5	0	100%	27-Mar-26 A	01-Apr-26 A																					
SUB-C1100	Excavation	18	0	100%	15-May-26 A	09-Jun-26 A																					
SUB-C1110	PCC & foundation concreting	29	0	100%	03-Jun-26 A	09-Jul-26 A																					
SUB-C1120	Plinth beam & backfilling	17	0	100%	21-Jul-26 A	08-Aug-26 A																					
SUB-C1130	Superstructure - RCC / steel erection	53	31	41%	19-Aug-26 A	07-Nov-26	98																				
SUB-C1150	Masonry & plastering	32	32	0%	01-Oct-26	10-Nov-26	118																				
SUB-C1140	Roofing & cladding	23	23	0%	03-Nov-26	30-Nov-26	101																				
SUB-C1160	MEP installation	48	48	0%	11-Nov-26	06-Jan-27	96																				
SUB-C1170	Finishes - flooring & painting	40	40	0%	01-Dec-26	16-Jan-27	101																				
SUB-C1180	Testing & commissioning	14	14	0%	07-Jan-27	22-Jan-27	96																				
SUB-C1190	Building handover to client	0	0	0%	22-Jan-27	22-Jan-27	96	Building handover to client																			
Utility Building		314		37%	25-Apr-26	04-May-27	11																				
Engineering		78		100%	14-May-26	12-Aug-26																					
UTL-E1010	Design basis & architectural layout	24	0	100%	14-May-26 A	15-Jun-26 A																					
UTL-E1020	Structural design & IFC drawings	35	0	100%	22-May-26 A	16-Jul-26 A																					
UTL-E1030	MEP design & drawings	38	0	100%	24-Jun-26 A	12-Aug-26 A																					
UTL-E1040	Drawing approval by client	13	0	100%	28-Jul-26 A	12-Aug-26 A																					
Procurement		169		21%	17-Jul-26	05-Feb-27	11																				
UTL-P1050	Structural steel - PO placement	14	0	100%	17-Jul-26 A	03-Aug-26 A																					
UTL-P1060	Structural steel - fabrication & supply to site	61	54	29%	04-Aug-26 A	05-Dec-26	46																				
UTL-P1070	MEP equipment - PO placement	17	12	44%	20-Aug-26 A	15-Oct-26	11																				
UTL-P1080	MEP equipment - manufacturing & delivery	93	93	0%	16-Oct-26	05-Feb-27	11																				
Construction		314		24%	25-Apr-26	04-May-27	11																				
UTL-C1090	Site mobilisation & survey	7	0	100%	25-Apr-26 A	02-May-26 A																					
UTL-C1100	Excavation	24	0	100%	04-Jun-26 A	01-Jul-26 A																					
UTL-C1110	PCC & foundation concreting	30	0	100%	16-Jun-26 A	27-Jul-26 A																					
UTL-C1120	Plinth beam & backfilling	21	0	100%	03-Aug-26 A	27-Aug-26 A																					

Actual work Remaining work Critical remaining Baseline Milestone Data Date Late start Overdue Future progress Invalid

Gantt layout (3/3)

[illegible]

Activities needing attention

Flag	Activity ID	Activity Name	Building	Status	Ref Start	Ref Finish	Finish	%	Concern / action
Overdue	ADM-C1170	Finishes - flooring & painting	Admin Building	In Progress	05-Aug-26	28-Sep-26	14-Oct-26	73%	Concern not raised
Overdue	WHS-C1130	Superstructure - RCC / steel erection	Warehouse Block	In Progress	24-Jun-26	10-Sep-26	01-Oct-26	99%	Concern not raised
Late start	WHS-C1140	Roofing & cladding	Warehouse Block	Not Started	05-Sep-26	13-Oct-26	10-Nov-26	0%	Concern not raised
Overdue	WHS-C1150	Masonry & plastering	Warehouse Block	In Progress	23-Jul-26	22-Sep-26	12-Oct-26	77%	Concern not raised
Overdue	SUB-P1060	Structural steel - fabrication & supply to site	33kV Substation	In Progress	01-Jul-26	17-Sep-26	01-Oct-26	98%	Concern not raised
Late start	SUB-C1150	Masonry & plastering	33kV Substation	Not Started	11-Sep-26	19-Oct-26	10-Nov-26	0%	Concern not raised
Overdue	UTL-P1070	MEP equipment - PO placement	Utility Building	In Progress	20-Aug-26	14-Sep-26	15-Oct-26	44%	Concern not raised
Late start	UTL-P1080	MEP equipment - manufacturing & delivery	Utility Building	Not Started	15-Sep-26	05-Jan-27	05-Feb-27	0%	Concern not raised
Late start	UTL-C1130	Superstructure - RCC / steel erection	Utility Building	Not Started	01-Sep-26	23-Nov-26	23-Dec-26	0%	Concern not raised
Late start	UTL-C1150	Masonry & plastering	Utility Building	Not Started	24-Sep-26	20-Nov-26	21-Dec-26	0%	Concern not raised
Overdue	STP-E1030	MEP design & drawings	STP & Pump House	In Progress	29-Jul-26	08-Sep-26	09-Oct-26	84%	Concern not raised
Overdue	STP-E1040	Drawing approval by client	STP & Pump House	In Progress	12-Aug-26	08-Sep-26	09-Oct-26	95%	Concern not raised
Overdue	STP-P1070	MEP equipment - PO placement	STP & Pump House	Not Started	09-Sep-26	21-Sep-26	23-Oct-26	0%	Concern not raised
Late start	STP-P1070	MEP equipment - PO placement	STP & Pump House	Not Started	09-Sep-26	21-Sep-26	23-Oct-26	0%	Concern not raised
Late start	STP-P1080	MEP equipment - manufacturing & delivery	STP & Pump House	Not Started	22-Sep-26	28-Nov-26	30-Dec-26	0%	Concern not raised
Overdue	STP-C1110	PCC & foundation concreting	STP & Pump House	In Progress	06-Aug-26	17-Sep-26	19-Oct-26	58%	Concern not raised
Late start	STP-C1120	Plinth beam & backfilling	STP & Pump House	Not Started	18-Sep-26	06-Oct-26	06-Nov-26	0%	Concern not raised
Future progress	STP-C1150	Masonry & plastering	STP & Pump House	In Progress	26-Aug-26	07-Dec-26	07-Jan-27	5%	Concern not raised
Out of sequence	STP-C1150	Masonry & plastering	STP & Pump House	In Progress	26-Aug-26	07-Dec-26	07-Jan-27	5%	Concern not raised
Future progress	STP-C1160	MEP installation	STP & Pump House	In Progress	26-Aug-26	16-Jan-27	17-Feb-27	5%	Concern not raised
Out of sequence	STP-C1160	MEP installation	STP & Pump House	In Progress	26-Aug-26	16-Jan-27	17-Feb-27	5%	Concern not raised

4-week look-ahead from 01-Oct-2026

Activity ID	Activity Name	Building	EPC	Status	Start	Finish	Rem Dur	%	TF
MPB-P1060	Structural steel - fabrication & supply to site	Main Process Building	Procurement	In Progress	15-Jun-26	23-Oct-26	18	82%	34
WHS-C1130	Superstructure - RCC / steel erection	Warehouse Block	Construction	In Progress	24-Jun-26	01-Oct-26	1	99%	79
SUB-P1060	Structural steel - fabrication & supply to site	33kV Substation	Procurement	In Progress	01-Jul-26	01-Oct-26	1	98%	83
MPB-C1130	Superstructure - RCC / steel erection	Main Process Building	Construction	In Progress	08-Jul-26	30-Nov-26	49	52%	49
WHS-P1080	MEP equipment - manufacturing & delivery	Warehouse Block	Procurement	In Progress	09-Jul-26	10-Nov-26	32	62%	77
WHS-C1150	Masonry & plastering	Warehouse Block	Construction	In Progress	23-Jul-26	12-Oct-26	9	77%	99
STP-E1030	MEP design & drawings	STP & Pump House	Engineering	In Progress	29-Jul-26	09-Oct-26	6	84%	51
ADM-C1160	MEP installation	Admin Building	Construction	In Progress	04-Aug-26	23-Oct-26	18	62%	158
UTL-P1060	Structural steel - fabrication & supply to site	Utility Building	Procurement	In Progress	04-Aug-26	05-Dec-26	54	29%	46
ADM-C1170	Finishes - flooring & painting	Admin Building	Construction	In Progress	05-Aug-26	14-Oct-26	11	73%	179
MPB-C1150	Masonry & plastering	Main Process Building	Construction	In Progress	06-Aug-26	13-Nov-26	35	49%	81
STP-C1110	PCC & foundation concreting	STP & Pump House	Construction	In Progress	06-Aug-26	19-Oct-26	15	58%	72
SUB-P1080	MEP equipment - manufacturing & delivery	33kV Substation	Procurement	In Progress	07-Aug-26	10-Nov-26	32	49%	96
STP-E1040	Drawing approval by client	STP & Pump House	Engineering	In Progress	12-Aug-26	09-Oct-26	1	95%	151
MPB-P1080	MEP equipment - manufacturing & delivery	Main Process Building	Procurement	In Progress	18-Aug-26	19-Jan-27	91	27%	0
SUB-C1130	Superstructure - RCC / steel erection	33kV Substation	Construction	In Progress	19-Aug-26	07-Nov-26	31	41%	98
UTL-P1070	MEP equipment - PO placement	Utility Building	Procurement	In Progress	20-Aug-26	15-Oct-26	12	44%	11
STP-C1150	Masonry & plastering	STP & Pump House	Construction	In Progress	26-Aug-26	07-Jan-27	31	5%	76
STP-C1160	MEP installation	STP & Pump House	Construction	In Progress	26-Aug-26	17-Feb-27	41	5%	62
STP-P1060	Structural steel - fabrication & supply to site	STP & Pump House	Procurement	In Progress	29-Aug-26	21-Nov-26	42	5%	87
SUB-C1150	Masonry & plastering	33kV Substation	Construction	Not Started	01-Oct-26	10-Nov-26	32	0%	118
UTL-C1130	Superstructure - RCC / steel erection	Utility Building	Construction	Not Started	01-Oct-26	23-Dec-26	69	0%	61
WHS-C1140	Roofing & cladding	Warehouse Block	Construction	Not Started	01-Oct-26	10-Nov-26	32	0%	116
STP-P1070	MEP equipment - PO placement	STP & Pump House	Procurement	Not Started	10-Oct-26	23-Oct-26	11	0%	62
UTL-P1080	MEP equipment - manufacturing & delivery	Utility Building	Procurement	Not Started	16-Oct-26	05-Feb-27	93	0%	11
STP-C1120	Plinth beam & backfilling	STP & Pump House	Construction	Not Started	21-Oct-26	06-Nov-26	15	0%	72
ADM-C1180	Testing & commissioning	Admin Building	Construction	Not Started	24-Oct-26	10-Nov-26	14	0%	158
STP-P1080	MEP equipment - manufacturing & delivery	STP & Pump House	Procurement	Not Started	24-Oct-26	30-Dec-26	56	0%	62
UTL-C1150	Masonry & plastering	Utility Building	Construction	Not Started	27-Oct-26	21-Dec-26	47	0%	86

Schedule health check - score 46%

Check	Result	Count	Of	%	Guideline
Missing logic (open ends)	PASS	0	55	0.0	Activities without a predecessor or a successor (first/last milestones excepted). Target <= 5%.
Leads (negative lags)	FAIL	6	156	3.8	Relationships with a negative lag hide logic. Target 0.
Positive lags	FAIL	46	156	29.5	Lags should be replaced with activities where possible. Target <= 5%.
Relationship types (FS >= 90%)	FAIL	48	156	69.2	Finish-to-Start should dominate. Shows the share of FS links.
Hard constraints	PASS	0	55	0.0	Must/finish-on or before constraints block logic. Target <= 5%.
High float (> 44 days)	FAIL	44	55	80.0	Usually means missing successors. Target <= 5%.
Negative float	PASS	0	55	0.0	Project is late against a constraint / must-finish date. Target 0.
High duration (> 44 days)	FAIL	20	55	36.4	Break long activities down for better control. Target <= 5%.
Invalid dates	PASS	0	116	0.0	Actuals after the Data Date or forecasts before it. Target 0.
Missed activities (finished late vs baseline)	FAIL	82	84	97.6	Planned to finish by the Data Date but finished late or not at all. Target <= 5%.
Critical path exists	PASS	5	55	9.1	A continuous critical path should drive the finish.
Baseline Execution Index (BEI >= 0.95)	FAIL	61	84	72.6	Activities completed / activities that should have been completed. 0.73
Logic loops	PASS	0	116	0.0	No circular logic.
