

Monthly Progress Summary

Planned %

74.6%

Actual %

57.6%

Variance

-17.0%

Forecast finish

19-Jun-27

Completed

96 / 173

In progress

29

Late start

11


Overdue

13


Critical

6

S-curve - cumulative progress (duration weighted)

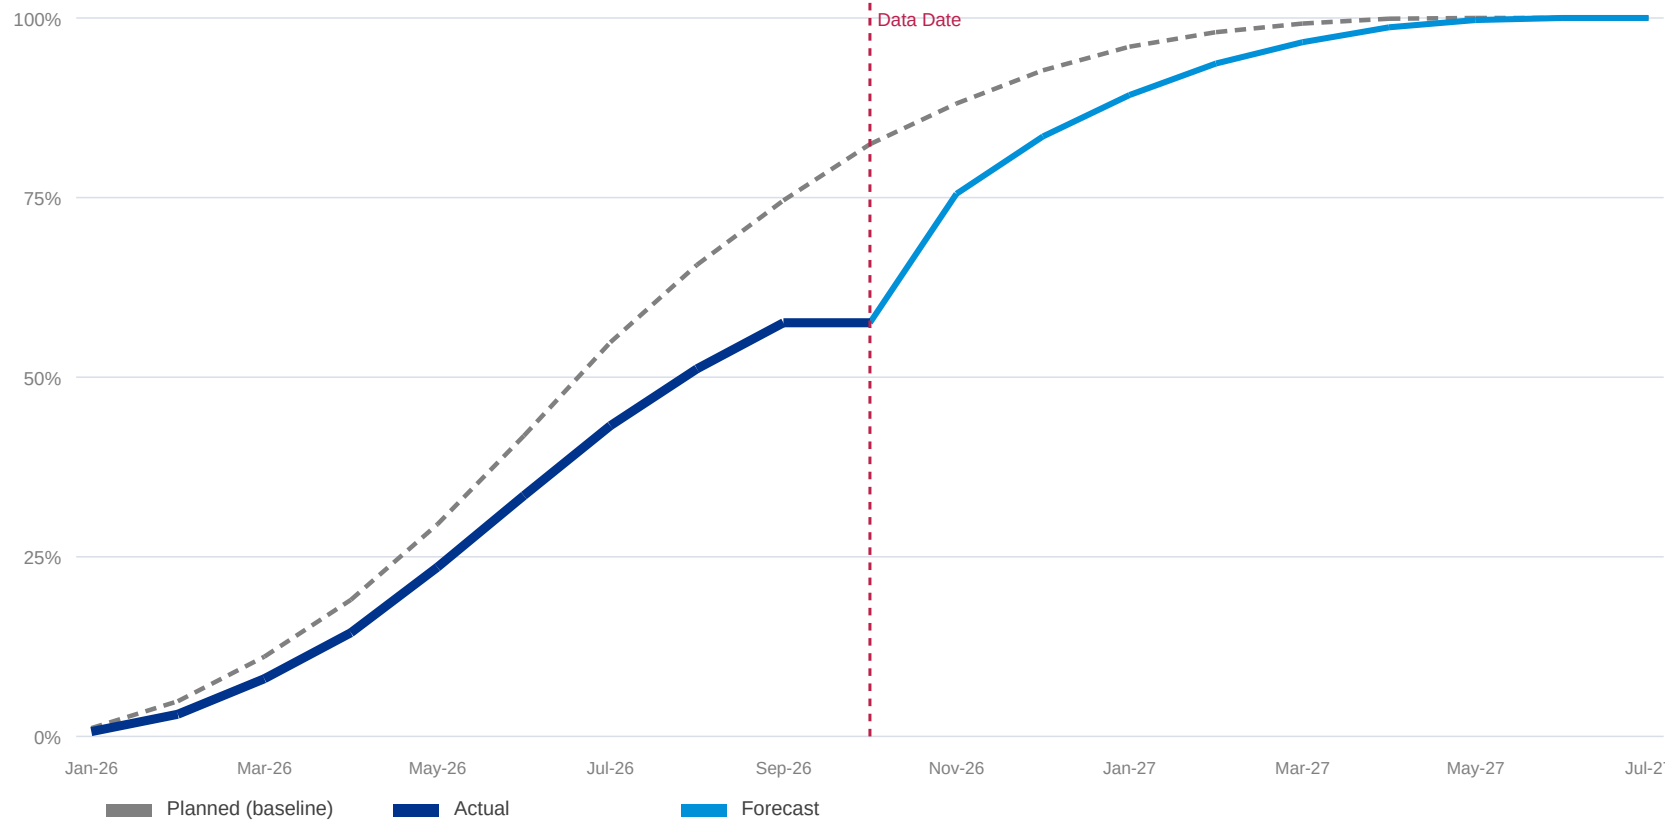

Building-wise progress (planned vs actual)

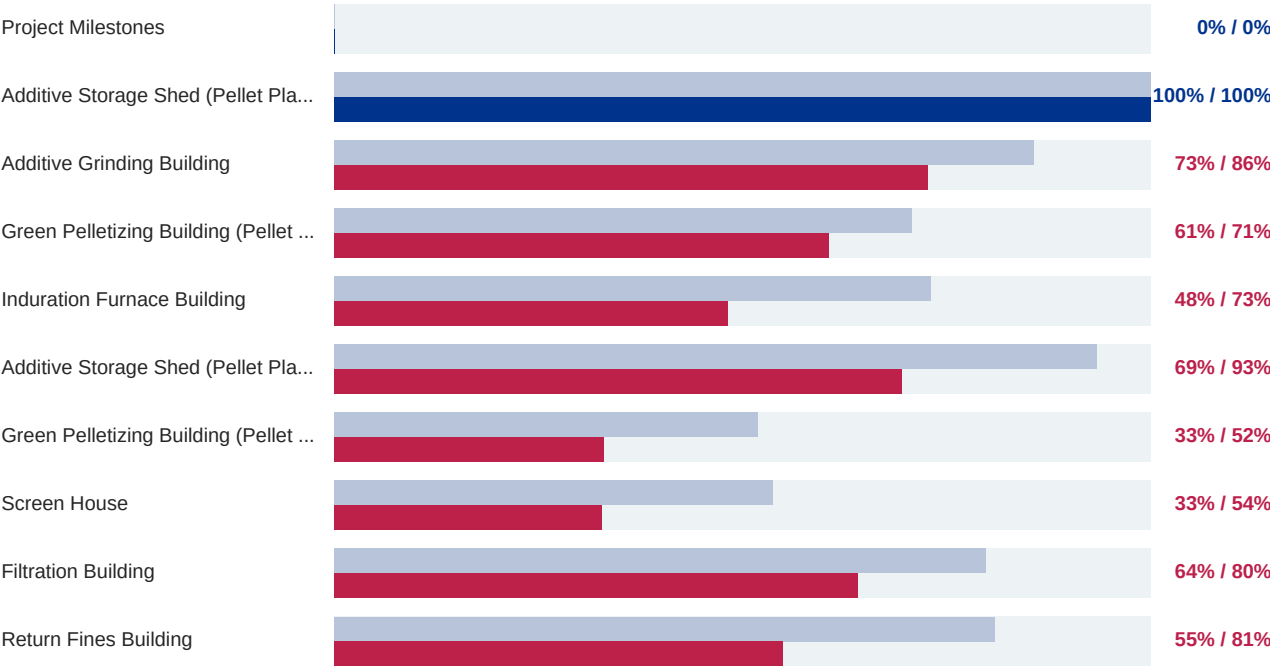

EPC-wise progress

EPC	Activities	Planned %	Actual %	Variance	Late start	Overdue
Engineering	36	100.0	99.7	-0.3	0	2
Procurement	36	83.8	56.8	-27.0	5	4
Construction	99	61.3	43.9	-17.4	6	7
Others	2	0.0	0.0	+0.0	0	0


Engine insights

- Overall progress is 57.6% against a planned 74.6% as of 01-Oct-2026 (-17.0%). Progress gained this period: 3.0%.
- 11 activities were due to start before the Data Date but have not started.
- 13 activities are past their finish date and still open.
- 2 future activities show progress - check these were really started early.
- 28 activities still need your update this month.
- 3 activities are progressing out of sequence.
- Return Fines Building is the most behind: 55.0% vs 80.9% planned (-25.9%).
- Additive Storage Shed (Pellet Plant-1) is on/ahead of plan at 100.0% (+0.0%).
- EPC progress: Engineering 100%, Procurement 57%, Construction 44%.
- Forecast project finish: 19-Jun-2027 - 37 working days later than baseline.
- 9 milestones are forecast late; worst: FLT-RFB-C1190 Building handover to client (16-Dec-26 -> 20-Feb-27).
- 6 activities are critical. Watch them in the look-ahead.

Gantt layout (2/4)

Activity ID	Activity Name	OD	RD	%	Start	Finish	TF	2026												2027							
								J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A
PP1-GPB-E1040	Drawing approval by client	21	0	100%	18-May-26 A	09-Jul-26 A																					
Procurement		211		65%	01-May-26	07-Jan-27	23																				
PP1-GPB-P1050	Structural steel - PO placement	19	0	100%	01-May-26 A	26-May-26 A																					
PP1-GPB-P1060	Structural steel - fabrication & supply to site	83	6	93%	01-Jun-26 A	08-Oct-26	59																				
PP1-GPB-P1070	MEP equipment - PO placement	26	0	100%	15-Jul-26 A	12-Aug-26 A																					
PP1-GPB-P1080	MEP equipment - manufacturing & delivery	118	81	31%	14-Aug-26 A	07-Jan-27	23																				
Construction		403		46%	29-Jan-26	24-May-27	23																				
PP1-GPB-C1090	Site mobilisation & survey	11	0	100%	29-Jan-26 A	10-Feb-26 A																					
PP1-GPB-C1100	Excavation	26	0	100%	03-Mar-26 A	02-Apr-26 A																					
PP1-GPB-C1110	PCC & foundation concreting	52	0	100%	14-Mar-26 A	18-May-26 A																					
PP1-GPB-C1120	Plinth beam & backfilling	29	0	100%	20-May-26 A	27-Jun-26 A																					
PP1-GPB-C1130	Superstructure - RCC / steel erection	94	21	78%	29-Jun-26 A	27-Oct-26	74																				
PP1-GPB-C1150	Masonry & plastering	59	22	63%	25-Jul-26 A	28-Oct-26	94																				
PP1-GPB-C1140	Roofing & cladding	46	46	0%	22-Oct-26	15-Dec-26	96																				
PP1-GPB-C1170	Finishes - flooring & painting	61	61	0%	16-Dec-26	26-Feb-27	96																				
PP1-GPB-C1160	MEP installation	89	89	0%	08-Jan-27	23-Apr-27	23																				
PP1-GPB-C1180	Testing & commissioning	26	26	0%	24-Apr-27	24-May-27	23																				
PP1-GPB-C1190	Building handover to client	0	0	0%	24-May-27	24-May-27	23																				
Induration Furnace Building		355		48%	02-Mar-26	29-Apr-27	44																				
Engineering		122		100%	16-Mar-26	05-Aug-26																					
PP1-IFB-E1010	Design basis & architectural layout	30	0	100%	16-Mar-26 A	28-Apr-26 A																					
PP1-IFB-E1020	Structural design & IFC drawings	39	0	100%	01-Apr-26 A	25-May-26 A																					
PP1-IFB-E1030	MEP design & drawings	52	0	100%	11-May-26 A	05-Aug-26 A																					
PP1-IFB-E1040	Drawing approval by client	18	0	100%	17-Jun-26 A	05-Aug-26 A																					
Procurement		200		40%	04-Jun-26	29-Jan-27	44																				
PP1-IFB-P1050	Structural steel - PO placement	19	0	100%	04-Jun-26 A	25-Jun-26 A																					
PP1-IFB-P1060	Structural steel - fabrication & supply to site	88	34	61%	03-Jul-26 A	12-Nov-26	62																				
PP1-IFB-P1070	MEP equipment - PO placement	23	6	72%	14-Aug-26 A	08-Oct-26	44																				
PP1-IFB-P1080	MEP equipment - manufacturing & delivery	93	93	0%	09-Oct-26	29-Jan-27	44																				
Construction		355		36%	02-Mar-26	29-Apr-27	44																				
PP1-IFB-C1090	Site mobilisation & survey	8	0	100%	02-Mar-26 A	12-Mar-26 A																					
PP1-IFB-C1100	Excavation	27	0	100%	27-Apr-26 A	26-May-26 A																					
PP1-IFB-C1110	PCC & foundation concreting	43	0	100%	12-May-26 A	27-Jun-26 A																					
PP1-IFB-C1120	Plinth beam & backfilling	26	0	100%	08-Jul-26 A	04-Aug-26 A																					
PP1-IFB-C1130	Superstructure - RCC / steel erection	79	52	34%	17-Aug-26 A	03-Dec-26	77																				
PP1-IFB-C1160	MEP installation	73	55	25%	26-Aug-26 A	05-Apr-27	44																				
PP1-IFB-C1150	Masonry & plastering	48	48	0%	01-Oct-26	28-Nov-26	111																				
PP1-IFB-C1140	Roofing & cladding	35	35	0%	28-Nov-26	08-Jan-27	77																				
PP1-IFB-C1170	Finishes - flooring & painting	60	60	0%	09-Jan-27	20-Mar-27	77																				
PP1-IFB-C1180	Testing & commissioning	21	21	0%	06-Apr-27	29-Apr-27	44																				
PP1-IFB-C1190	Building handover to client	0	0	0%	29-Apr-27	29-Apr-27	44																				
Pellet Plant-2		386		42%	18-Mar-26	19-Jun-27	0																				
Additive Storage Shed		244		69%	18-Mar-26	02-Jan-27	136																				
Engineering		59		100%	02-Apr-26	10-Jun-26																					
PP2-ASS-E1010	Design basis & architectural layout	17	0	100%	02-Apr-26 A	30-Apr-26 A																					
PP2-ASS-E1020	Structural design & IFC drawings	25	0	100%	16-Apr-26 A	27-May-26 A																					
PP2-ASS-E1030	MEP design & drawings	27	0	100%	01-May-26 A	10-Jun-26 A																					
PP2-ASS-E1040	Drawing approval by client	9	0	100%	29-May-26 A	10-Jun-26 A																					
Procurement		131		83%	28-May-26	30-Oct-26	142																				
PP2-ASS-P1050	Structural steel - PO placement	10	0	100%	28-May-26 A	09-Jun-26 A																					
PP2-ASS-P1060	Structural steel - fabrication & supply to site	43	0	100%	11-Jun-26 A	05-Aug-26 A																					
PP2-ASS-P1070	MEP equipment - PO placement	12	0	100%	15-Jun-26 A	27-Jun-26 A																					
PP2-ASS-P1080	MEP equipment - manufacturing & delivery	67	24	66%	02-Jul-26 A	30-Oct-26	142																				
Construction		244		52%	18-Mar-26	02-Jan-27	136																				
PP2-ASS-C1090	Site mobilisation & survey	5	0	100%	18-Mar-26 A	23-Mar-26 A																					
PP2-ASS-C1100	Excavation	17	0	100%	29-Apr-26 A	20-May-26 A																					

Gantt layout (3/4)

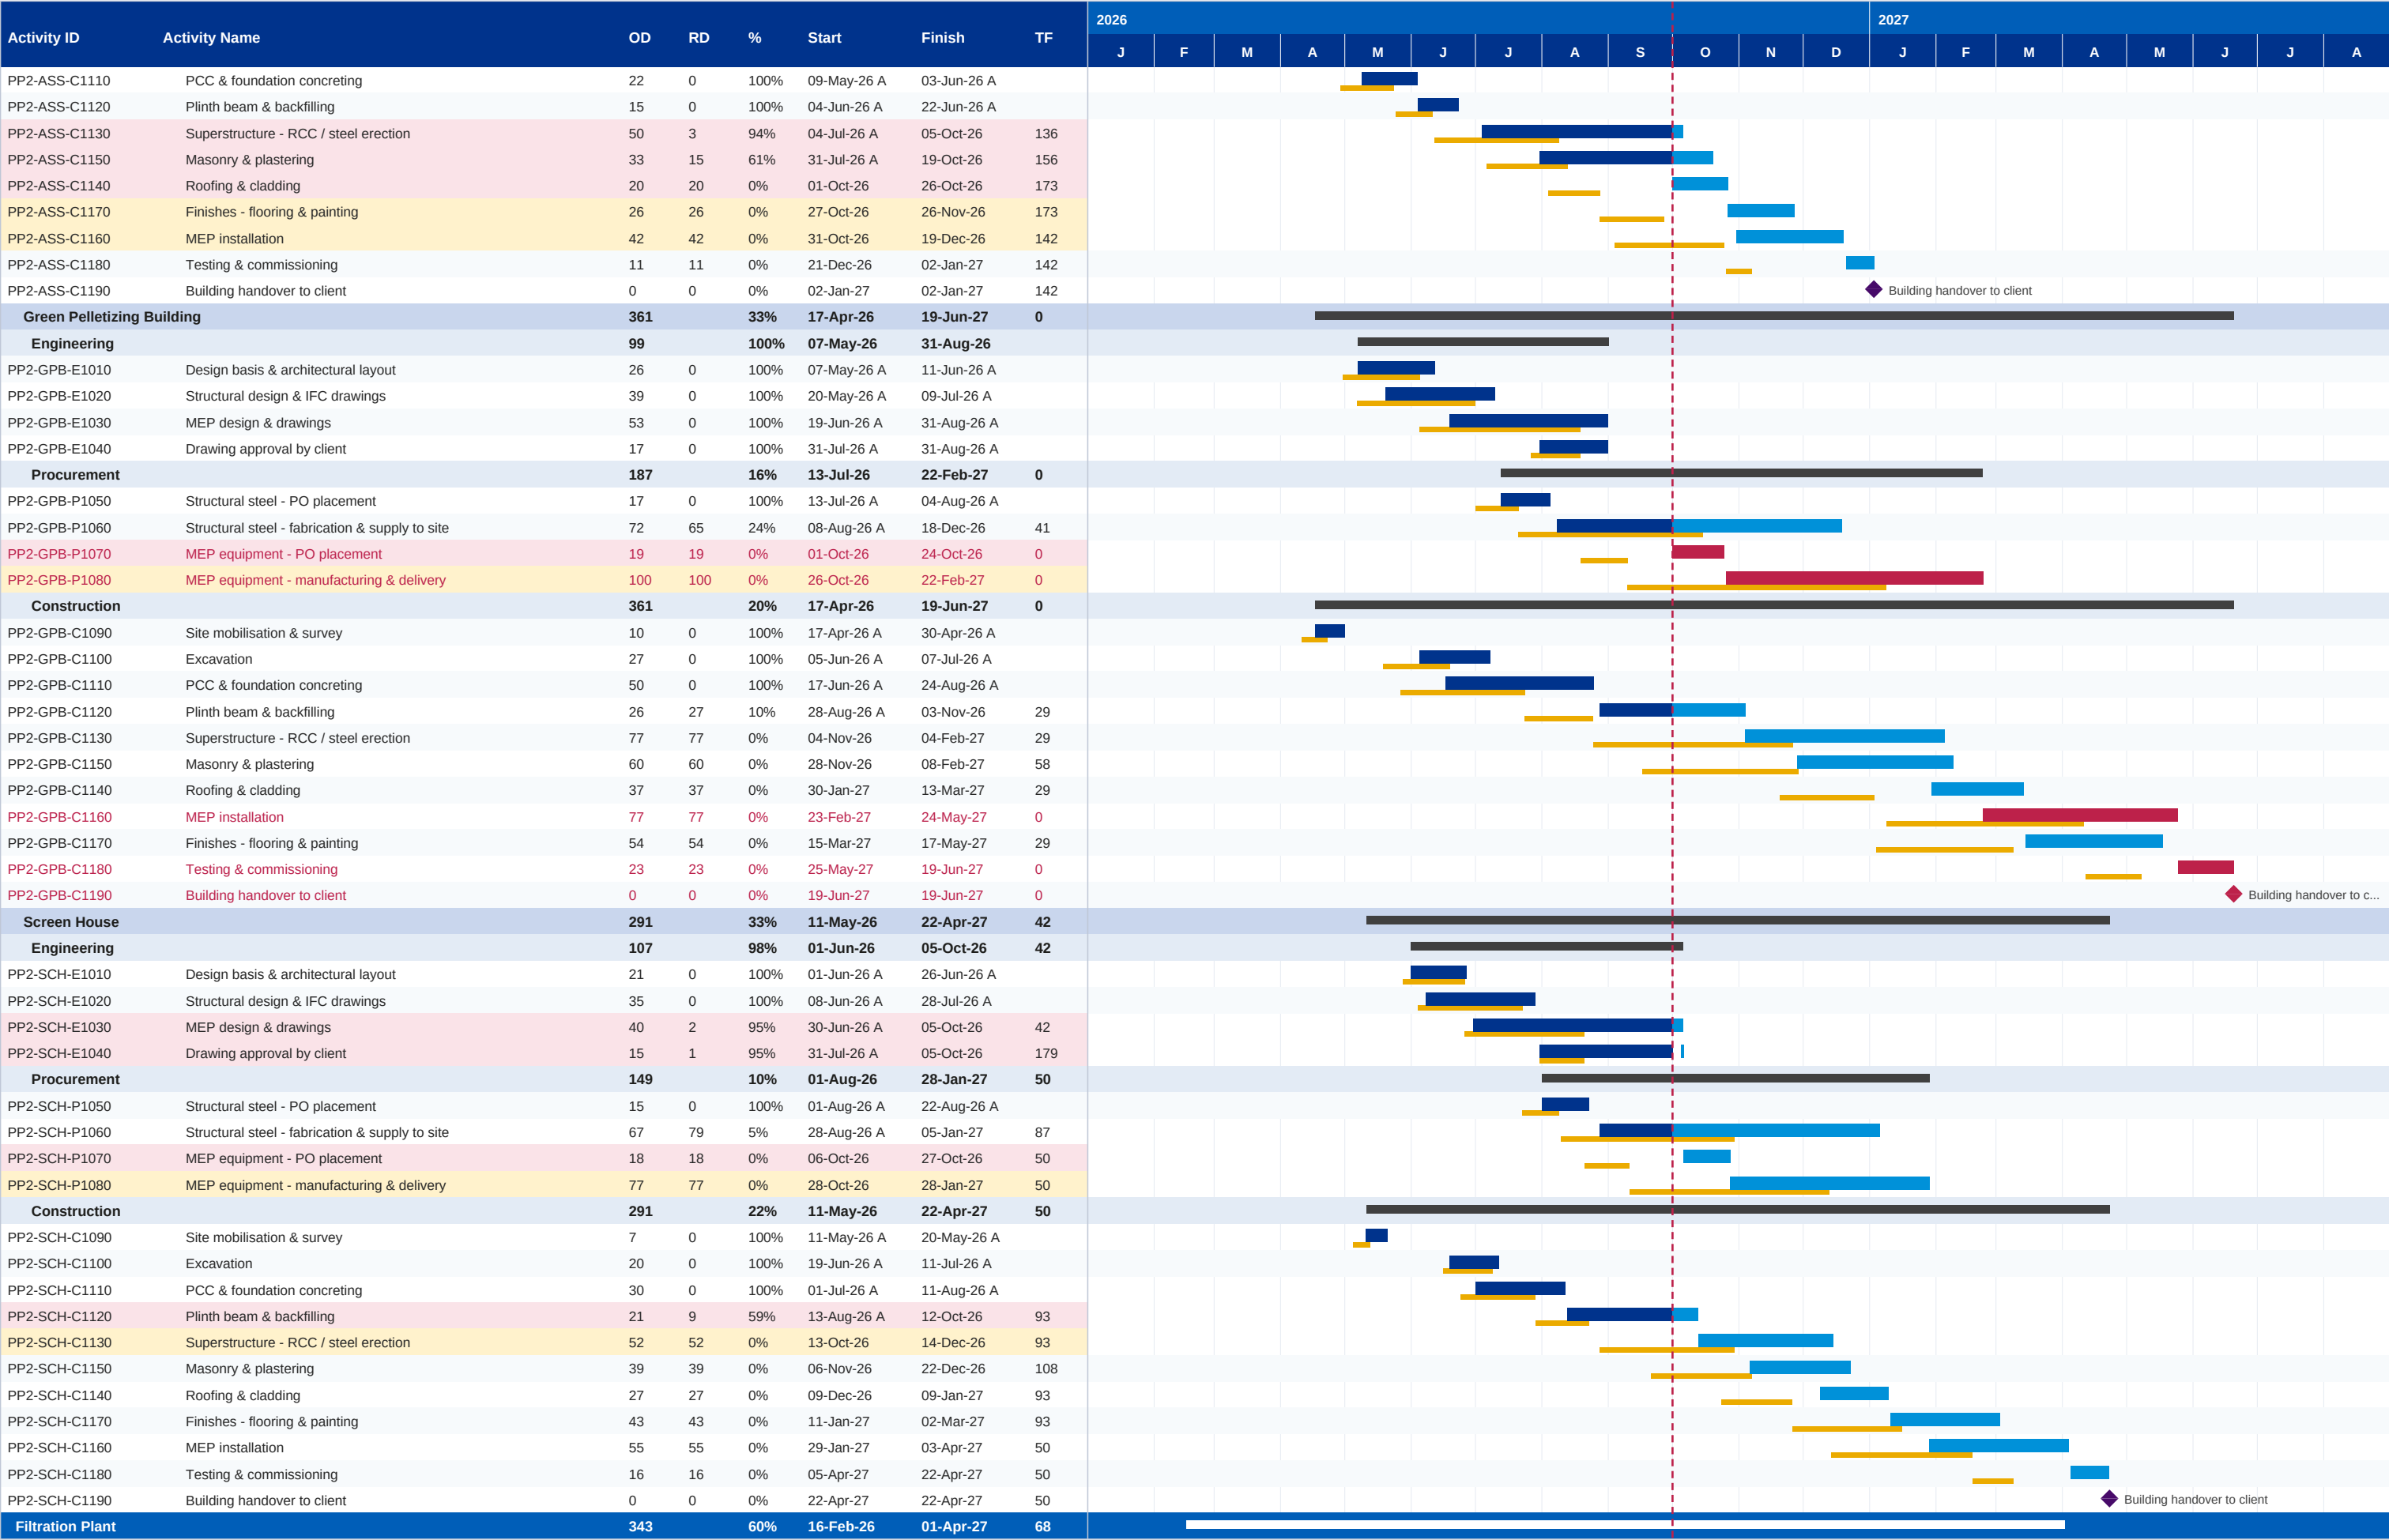

Actual work

Remaining work

Critical remaining

Baseline

Milestone

Data Date

Late start

Overdue

Future progress

Invalid

Gantt layout (4/4)

Activity ID	Activity Name	OD	RD	%	Start	Finish	TF	2026													2027										
								J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A				
Filtration Building		343		64%	16-Feb-26	01-Apr-27	68																								
Engineering		97		100%	17-Feb-26	11-Jun-26																									
FLT-FLB-E1010	Design basis & architectural layout	24	0	100%	17-Feb-26 A	20-Mar-26 A																									
FLT-FLB-E1020	Structural design & IFC drawings	39	0	100%	24-Feb-26 A	30-Apr-26 A																									
FLT-FLB-E1030	MEP design & drawings	53	0	100%	27-Mar-26 A	04-Jun-26 A																									
FLT-FLB-E1040	Drawing approval by client	16	0	100%	18-May-26 A	11-Jun-26 A																									
Procurement		190		75%	05-May-26	16-Dec-26	68																								
FLT-FLB-P1050	Structural steel - PO placement	18	0	100%	05-May-26 A	26-May-26 A																									
FLT-FLB-P1060	Structural steel - fabrication & supply to site	66	0	100%	27-May-26 A	20-Aug-26 A																									
FLT-FLB-P1070	MEP equipment - PO placement	20	0	100%	06-Jun-26 A	27-Jun-26 A																									
FLT-FLB-P1080	MEP equipment - manufacturing & delivery	89	63	45%	04-Jul-26 A	16-Dec-26	68																								
Construction		343		47%	16-Feb-26	01-Apr-27	68																								
FLT-FLB-C1090	Site mobilisation & survey	8	0	100%	16-Feb-26 A	26-Feb-26 A																									
FLT-FLB-C1100	Excavation	25	0	100%	10-Mar-26 A	14-Apr-26 A																									
FLT-FLB-C1110	PCC & foundation concreting	39	0	100%	23-Mar-26 A	14-May-26 A																									
FLT-FLB-C1120	Plinth beam & backfilling	26	0	100%	20-May-26 A	22-Jun-26 A																									
FLT-FLB-C1130	Superstructure - RCC / steel erection	67	27	66%	25-Jun-26 A	03-Nov-26	101																								
FLT-FLB-C1150	Masonry & plastering	46	16	73%	22-Jul-26 A	21-Oct-26	121																								
FLT-FLB-C1160	MEP installation	69	67	5%	26-Aug-26 A	06-Mar-27	68																								
FLT-FLB-C1140	Roofing & cladding	34	34	0%	29-Oct-26	08-Dec-26	113																								
FLT-FLB-C1170	Finishes - flooring & painting	50	50	0%	09-Dec-26	06-Feb-27	113																								
FLT-FLB-C1180	Testing & commissioning	21	21	0%	08-Mar-27	01-Apr-27	68																								
FLT-FLB-C1190	Building handover to client	0	0	0%	01-Apr-27	01-Apr-27	68				◆ Building handover to client																				
Return Fines Building		271		55%	04-Apr-26	20-Feb-27	101																								
Engineering		74		100%	16-Apr-26	10-Jul-26																									
FLT-RFB-E1010	Design basis & architectural layout	19	0	100%	16-Apr-26 A	13-May-26 A																									
FLT-RFB-E1020	Structural design & IFC drawings	34	0	100%	23-Apr-26 A	10-Jun-26 A																									
FLT-RFB-E1030	MEP design & drawings	36	0	100%	19-May-26 A	10-Jul-26 A																									
FLT-RFB-E1040	Drawing approval by client	11	0	100%	22-Jun-26 A	10-Jul-26 A																									
Procurement		146		56%	12-Jun-26	03-Dec-26	101																								
FLT-RFB-P1050	Structural steel - PO placement	11	0	100%	12-Jun-26 A	24-Jun-26 A																									
FLT-RFB-P1060	Structural steel - fabrication & supply to site	60	28	62%	30-Jun-26 A	04-Nov-26	108																								
FLT-RFB-P1070	MEP equipment - PO placement	12	0	100%	11-Jul-26 A	24-Jul-26 A																									
FLT-RFB-P1080	MEP equipment - manufacturing & delivery	62	52	34%	29-Jul-26 A	03-Dec-26	101																								
Construction		271		39%	04-Apr-26	20-Feb-27	101																								
FLT-RFB-C1090	Site mobilisation & survey	7	0	100%	04-Apr-26 A	11-Apr-26 A																									
FLT-RFB-C1100	Excavation	17	0	100%	05-May-26 A	27-May-26 A																									
FLT-RFB-C1110	PCC & foundation concreting	27	0	100%	14-May-26 A	13-Jun-26 A																									
FLT-RFB-C1120	Plinth beam & backfilling	20	0	100%	17-Jun-26 A	08-Jul-26 A																									
FLT-RFB-C1130	Superstructure - RCC / steel erection	58	34	43%	22-Jul-26 A	12-Nov-26	123																								
FLT-RFB-C1150	Masonry & plastering	34	25	40%	14-Aug-26 A	31-Oct-26	143																								
FLT-RFB-C1140	Roofing & cladding	23	23	0%	06-Nov-26	03-Dec-26	135																								
FLT-RFB-C1160	MEP installation	53	53	0%	04-Dec-26	05-Feb-27	101																								
FLT-RFB-C1170	Finishes - flooring & painting	32	32	0%	04-Dec-26	11-Jan-27	135																								
FLT-RFB-C1180	Testing & commissioning	13	13	0%	06-Feb-27	20-Feb-27	101																								
FLT-RFB-C1190	Building handover to client	0	0	0%	20-Feb-27	20-Feb-27	101				◆ Building handover to client																				

Activities needing attention

Flag	Activity ID	Activity Name	Building	Status	Ref Start	Ref Finish	Finish	%	Concern / action
Out of sequence	PP1-AGB-C1140	Roofing & cladding	Additive Grinding Building	In Progress	28-Sep-26	04-Nov-26	07-Nov-26	15%	Concern not raised
Overdue	PP1-AGB-C1150	Masonry & plastering	Additive Grinding Building	In Progress	11-Jul-26	24-Sep-26	12-Oct-26	84%	Concern not raised
Overdue	PP1-IFB-P1070	MEP equipment - PO placement	Induration Furnace Building	In Progress	14-Aug-26	12-Sep-26	08-Oct-26	72%	Concern not raised
Late start	PP1-IFB-P1080	MEP equipment - manufacturing & delivery	Induration Furnace Building	Not Started	14-Sep-26	04-Jan-27	29-Jan-27	0%	Concern not raised
Late start	PP1-IFB-C1150	Masonry & plastering	Induration Furnace Building	Not Started	09-Sep-26	05-Nov-26	28-Nov-26	0%	Concern not raised
Future progress	PP1-IFB-C1160	MEP installation	Induration Furnace Building	In Progress	26-Aug-26	30-Mar-27	05-Apr-27	25%	Concern not raised
Out of sequence	PP1-IFB-C1160	MEP installation	Induration Furnace Building	In Progress	26-Aug-26	30-Mar-27	05-Apr-27	25%	Concern not raised
Overdue	PP2-ASS-P1080	MEP equipment - manufacturing & delivery	Additive Storage Shed (Pellet Plant-2)	In Progress	02-Jul-26	28-Sep-26	30-Oct-26	66%	Concern not raised
Overdue	PP2-ASS-C1130	Superstructure - RCC / steel erection	Additive Storage Shed (Pellet Plant-2)	In Progress	04-Jul-26	03-Sep-26	05-Oct-26	94%	Concern not raised
Overdue	PP2-ASS-C1140	Roofing & cladding	Additive Storage Shed (Pellet Plant-2)	Not Started	01-Sep-26	23-Sep-26	26-Oct-26	0%	Concern not raised
Late start	PP2-ASS-C1140	Roofing & cladding	Additive Storage Shed (Pellet Plant-2)	Not Started	01-Sep-26	23-Sep-26	26-Oct-26	0%	Concern not raised
Overdue	PP2-ASS-C1150	Masonry & plastering	Additive Storage Shed (Pellet Plant-2)	In Progress	31-Jul-26	17-Sep-26	19-Oct-26	61%	Concern not raised
Late start	PP2-ASS-C1160	MEP installation	Additive Storage Shed (Pellet Plant-2)	Not Started	29-Sep-26	19-Nov-26	19-Dec-26	0%	Concern not raised
Late start	PP2-ASS-C1170	Finishes - flooring & painting	Additive Storage Shed (Pellet Plant-2)	Not Started	24-Sep-26	26-Oct-26	26-Nov-26	0%	Concern not raised
Overdue	PP2-GPB-P1070	MEP equipment - PO placement	Green Pelletizing Building (Pellet Plant-2)	Not Started	01-Sep-26	22-Sep-26	24-Oct-26	0%	Concern not raised
Late start	PP2-GPB-P1070	MEP equipment - PO placement	Green Pelletizing Building (Pellet Plant-2)	Not Started	01-Sep-26	22-Sep-26	24-Oct-26	0%	Concern not raised
Late start	PP2-GPB-P1080	MEP equipment - manufacturing & delivery	Green Pelletizing Building (Pellet Plant-2)	Not Started	23-Sep-26	21-Jan-27	22-Feb-27	0%	Concern not raised
Overdue	PP2-SCH-E1030	MEP design & drawings	Screen House	In Progress	30-Jun-26	02-Sep-26	05-Oct-26	95%	Concern not raised
Overdue	PP2-SCH-E1040	Drawing approval by client	Screen House	In Progress	31-Jul-26	02-Sep-26	05-Oct-26	95%	Concern not raised
Overdue	PP2-SCH-P1070	MEP equipment - PO placement	Screen House	Not Started	03-Sep-26	23-Sep-26	27-Oct-26	0%	Concern not raised
Late start	PP2-SCH-P1070	MEP equipment - PO placement	Screen House	Not Started	03-Sep-26	23-Sep-26	27-Oct-26	0%	Concern not raised
Late start	PP2-SCH-P1080	MEP equipment - manufacturing & delivery	Screen House	Not Started	24-Sep-26	26-Dec-26	28-Jan-27	0%	Concern not raised
Overdue	PP2-SCH-C1120	Plinth beam & backfilling	Screen House	In Progress	13-Aug-26	10-Sep-26	12-Oct-26	59%	Concern not raised
Late start	PP2-SCH-C1130	Superstructure - RCC / steel erection	Screen House	Not Started	15-Sep-26	17-Nov-26	14-Dec-26	0%	Concern not raised
Late start	FLT-FLB-C1140	Roofing & cladding	Filtration Building	Not Started	26-Sep-26	06-Nov-26	08-Dec-26	0%	Concern not raised
Overdue	FLT-FLB-C1150	Masonry & plastering	Filtration Building	In Progress	22-Jul-26	18-Sep-26	21-Oct-26	73%	Concern not raised
Future progress	FLT-FLB-C1160	MEP installation	Filtration Building	In Progress	26-Aug-26	04-Feb-27	06-Mar-27	5%	Concern not raised
Out of sequence	FLT-FLB-C1160	MEP installation	Filtration Building	In Progress	26-Aug-26	04-Feb-27	06-Mar-27	5%	Concern not raised
Overdue	FLT-RFB-C1150	Masonry & plastering	Return Fines Building	In Progress	14-Aug-26	29-Sep-26	31-Oct-26	40%	Concern not raised

4-week look-ahead from 01-Oct-2026

Activity ID	Activity Name	Building	EPC	Status	Start	Finish	Rem Dur	%	TF
PP1-GPB-P1060	Structural steel - fabrication & supply to site	Green Pelletizing Building (Pellet Plant-1)	Procurement	In Progress	01-Jun-26	08-Oct-26	6	93%	59
PP1-AGB-C1130	Superstructure - RCC / steel erection	Additive Grinding Building	Construction	In Progress	13-Jun-26	13-Oct-26	10	88%	109
PP1-AGB-P1080	MEP equipment - manufacturing & delivery	Additive Grinding Building	Procurement	In Progress	22-Jun-26	07-Nov-26	31	69%	108
FLT-FLB-C1130	Superstructure - RCC / steel erection	Filtration Building	Construction	In Progress	25-Jun-26	03-Nov-26	27	66%	101
PP1-GPB-C1130	Superstructure - RCC / steel erection	Green Pelletizing Building (Pellet Plant-1)	Construction	In Progress	29-Jun-26	27-Oct-26	21	78%	74
FLT-RFB-P1060	Structural steel - fabrication & supply to site	Return Fines Building	Procurement	In Progress	30-Jun-26	04-Nov-26	28	62%	108
PP2-SCH-E1030	MEP design & drawings	Screen House	Engineering	In Progress	30-Jun-26	05-Oct-26	2	95%	42
PP2-ASS-P1080	MEP equipment - manufacturing & delivery	Additive Storage Shed (Pellet Plant-2)	Procurement	In Progress	02-Jul-26	30-Oct-26	24	66%	142
PP1-IFB-P1060	Structural steel - fabrication & supply to site	Induration Furnace Building	Procurement	In Progress	03-Jul-26	12-Nov-26	34	61%	62
FLT-FLB-P1080	MEP equipment - manufacturing & delivery	Filtration Building	Procurement	In Progress	04-Jul-26	16-Dec-26	63	45%	68
PP2-ASS-C1130	Superstructure - RCC / steel erection	Additive Storage Shed (Pellet Plant-2)	Construction	In Progress	04-Jul-26	05-Oct-26	3	94%	136
PP1-AGB-C1150	Masonry & plastering	Additive Grinding Building	Construction	In Progress	11-Jul-26	12-Oct-26	9	84%	129
FLT-FLB-C1150	Masonry & plastering	Filtration Building	Construction	In Progress	22-Jul-26	21-Oct-26	16	73%	121
FLT-RFB-C1130	Superstructure - RCC / steel erection	Return Fines Building	Construction	In Progress	22-Jul-26	12-Nov-26	34	43%	123
PP1-GPB-C1150	Masonry & plastering	Green Pelletizing Building (Pellet Plant-1)	Construction	In Progress	25-Jul-26	28-Oct-26	22	63%	94
FLT-RFB-P1080	MEP equipment - manufacturing & delivery	Return Fines Building	Procurement	In Progress	29-Jul-26	03-Dec-26	52	34%	101
PP2-ASS-C1150	Masonry & plastering	Additive Storage Shed (Pellet Plant-2)	Construction	In Progress	31-Jul-26	19-Oct-26	15	61%	156
PP2-SCH-E1040	Drawing approval by client	Screen House	Engineering	In Progress	31-Jul-26	05-Oct-26	1	95%	179
PP2-GPB-P1060	Structural steel - fabrication & supply to site	Green Pelletizing Building (Pellet Plant-2)	Procurement	In Progress	08-Aug-26	18-Dec-26	65	24%	41
PP2-SCH-C1120	Plinth beam & backfilling	Screen House	Construction	In Progress	13-Aug-26	12-Oct-26	9	59%	93
FLT-RFB-C1150	Masonry & plastering	Return Fines Building	Construction	In Progress	14-Aug-26	31-Oct-26	25	40%	143
PP1-GPB-P1080	MEP equipment - manufacturing & delivery	Green Pelletizing Building (Pellet Plant-1)	Procurement	In Progress	14-Aug-26	07-Jan-27	81	31%	23
PP1-IFB-P1070	MEP equipment - PO placement	Induration Furnace Building	Procurement	In Progress	14-Aug-26	08-Oct-26	6	72%	44
PP1-IFB-C1130	Superstructure - RCC / steel erection	Induration Furnace Building	Construction	In Progress	17-Aug-26	03-Dec-26	52	34%	77
FLT-FLB-C1160	MEP installation	Filtration Building	Construction	In Progress	26-Aug-26	06-Mar-27	67	5%	68
PP1-IFB-C1160	MEP installation	Induration Furnace Building	Construction	In Progress	26-Aug-26	05-Apr-27	55	25%	44
PP2-GPB-C1120	Plinth beam & backfilling	Green Pelletizing Building (Pellet Plant-2)	Construction	In Progress	28-Aug-26	03-Nov-26	27	10%	29
PP2-SCH-P1060	Structural steel - fabrication & supply to site	Screen House	Procurement	In Progress	28-Aug-26	05-Jan-27	79	5%	87
PP1-AGB-C1140	Roofing & cladding	Additive Grinding Building	Construction	In Progress	28-Sep-26	07-Nov-26	26	15%	142
PP1-IFB-C1150	Masonry & plastering	Induration Furnace Building	Construction	Not Started	01-Oct-26	28-Nov-26	48	0%	111
PP2-ASS-C1140	Roofing & cladding	Additive Storage Shed (Pellet Plant-2)	Construction	Not Started	01-Oct-26	26-Oct-26	20	0%	173
PP2-GPB-P1070	MEP equipment - PO placement	Green Pelletizing Building (Pellet Plant-2)	Procurement	Not Started	01-Oct-26	24-Oct-26	19	0%	0
PP2-SCH-P1070	MEP equipment - PO placement	Screen House	Procurement	Not Started	06-Oct-26	27-Oct-26	18	0%	50
PP1-IFB-P1080	MEP equipment - manufacturing & delivery	Induration Furnace Building	Procurement	Not Started	09-Oct-26	29-Jan-27	93	0%	44
PP2-SCH-C1130	Superstructure - RCC / steel erection	Screen House	Construction	Not Started	13-Oct-26	14-Dec-26	52	0%	93
PP1-GPB-C1140	Roofing & cladding	Green Pelletizing Building (Pellet Plant-1)	Construction	Not Started	22-Oct-26	15-Dec-26	46	0%	96
PP2-GPB-P1080	MEP equipment - manufacturing & delivery	Green Pelletizing Building (Pellet Plant-2)	Procurement	Not Started	26-Oct-26	22-Feb-27	100	0%	0
PP2-ASS-C1170	Finishes - flooring & painting	Additive Storage Shed (Pellet Plant-2)	Construction	Not Started	27-Oct-26	26-Nov-26	26	0%	173
PP2-SCH-P1080	MEP equipment - manufacturing & delivery	Screen House	Procurement	Not Started	28-Oct-26	28-Jan-27	77	0%	50

Schedule health check - score 46%

Check	Result	Count	Of	%	Guideline
Missing logic (open ends)	PASS	0	77	0.0	Activities without a predecessor or a successor (first/last milestones excepted). Target <= 5%.
Leads (negative lags)	FAIL	9	234	3.8	Relationships with a negative lag hide logic. Target 0.
Positive lags	FAIL	70	234	29.9	Lags should be replaced with activities where possible. Target <= 5%.
Relationship types (FS >= 90%)	FAIL	72	234	69.2	Finish-to-Start should dominate. Shows the share of FS links.
Hard constraints	PASS	0	77	0.0	Must/finish-on or before constraints block logic. Target <= 5%.
High float (> 44 days)	FAIL	56	77	72.7	Usually means missing successors. Target <= 5%.
Negative float	PASS	0	77	0.0	Project is late against a constraint / must-finish date. Target 0.
High duration (> 44 days)	FAIL	39	77	50.6	Break long activities down for better control. Target <= 5%.
Invalid dates	PASS	0	173	0.0	Actuals after the Data Date or forecasts before it. Target 0.
Missed activities (finished late vs baseline)	FAIL	119	125	95.2	Planned to finish by the Data Date but finished late or not at all. Target <= 5%.
Critical path exists	PASS	6	77	7.8	A continuous critical path should drive the finish.
Baseline Execution Index (BEI >= 0.95)	FAIL	96	125	76.8	Activities completed / activities that should have been completed. 0.77
Logic loops	PASS	0	173	0.0	No circular logic.
